


USACE – ST PAUL DISTRICT LOWER POOL 2 & HEAD OF LAKE PEPIN CONCERNS

Presentation for

MISSISSIPPI MANAGERS MEETING

By Kristin Moe

7 February 2023




US Army Corps
of Engineers®

BUILDING STRONG®



CHANNEL MANAGEMENT STUDY LOWER POOL 2 – PHASE 2

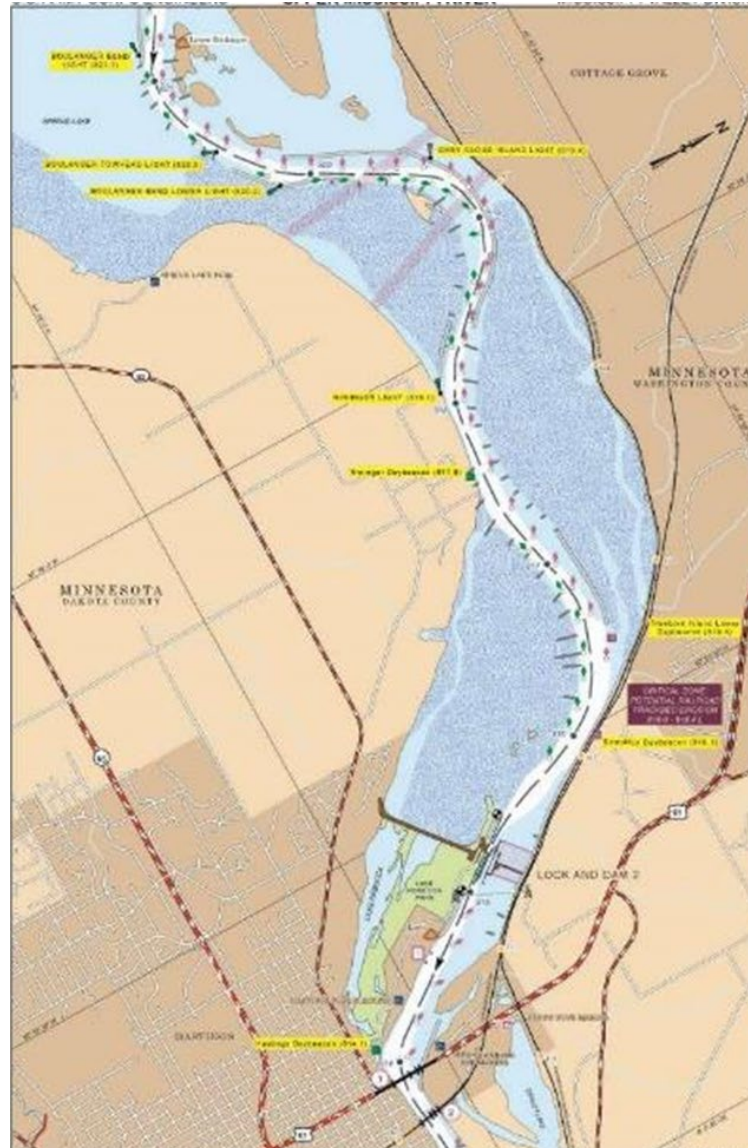

BUILDING STRONG®



POOL 2 CHANNEL IMPROVEMENT PROJECT



Rock structures – 2019 & 2020 construction

- Upper structure completed Nov 2018
- Lower structure completed Nov 2019

Dredging Phase

- Ongoing as budget and placement site capacity allows



BUILDING STRONG®



CHANNEL MANAGEMENT STUDY UPPER POOL 4



Potential features:

- Wing dams
- Rock revetment
- Rock closures

Draft schedule:

- Alternatives – MAY 2023
- Draft Report – AUG 2023
- Final Report – Fall 2024



BUILDING STRONG®
