

DN 15-23

DREDGING NOTICE
U.S. ARMY CORPS OF ENGINEERS
ST. PAUL DISTRICT

NOTICE DATE: July 27th, 2015

DREDGING CATEGORY: Imminent

MEETING DATE: If requested

MEETING TIME:

BOAT REQUIREMENT:

MEETING LOCATION:

DREDGE CUT NAME: Upper Approach to LD 7 RIVER MILE: 702.5 – 703.0

HISTORIC DATA

Frequency: 7 %

Avg. Quantity/Job: 10,815 yd³

Date Last Dredged: August 29th, 2012

Avg. Quantity/Year: 721 yd³

SURVEY DATA

Date Surveyed: July 20th, 2015

Water Surface Elevation: 638.6

Low Control Pool Elevation: 638.5

Net Difference: + 0.1'

5 Day River Forecast: Holding steady

DREDGING DATA

Recommended Channel Width: 300

Recommended Dredging Depth: 13 feet

Estimated Quantity: 15,796 yd³

Type of Dredge: Contract Mechanical

Proposed Dredging Date: July 27th, 2015

Estimated Duration: 8 dredging days

Justification for Dredging: Channel has been reduced 200' between the 10.5' contours and 290' between the 9' contours.

MATERIAL PLACEMENT DATA

Proposed Placement Site: Trempealeau

Locations: 7-714.1-LWP


Site Characteristics: This is a historically used upland beneficial use site.


If you have any questions concerning this project or request an on-site meeting; please call me at (651) 290-5155.

Dan Cottrell
Channel Maintenance Coordinator

Pool 7, Upper Approach to LD 7
River Mile: 702.5 - 703.0
Date Surveyed: July 20th, 2015
Scale: 1" = 200'

CUT-1

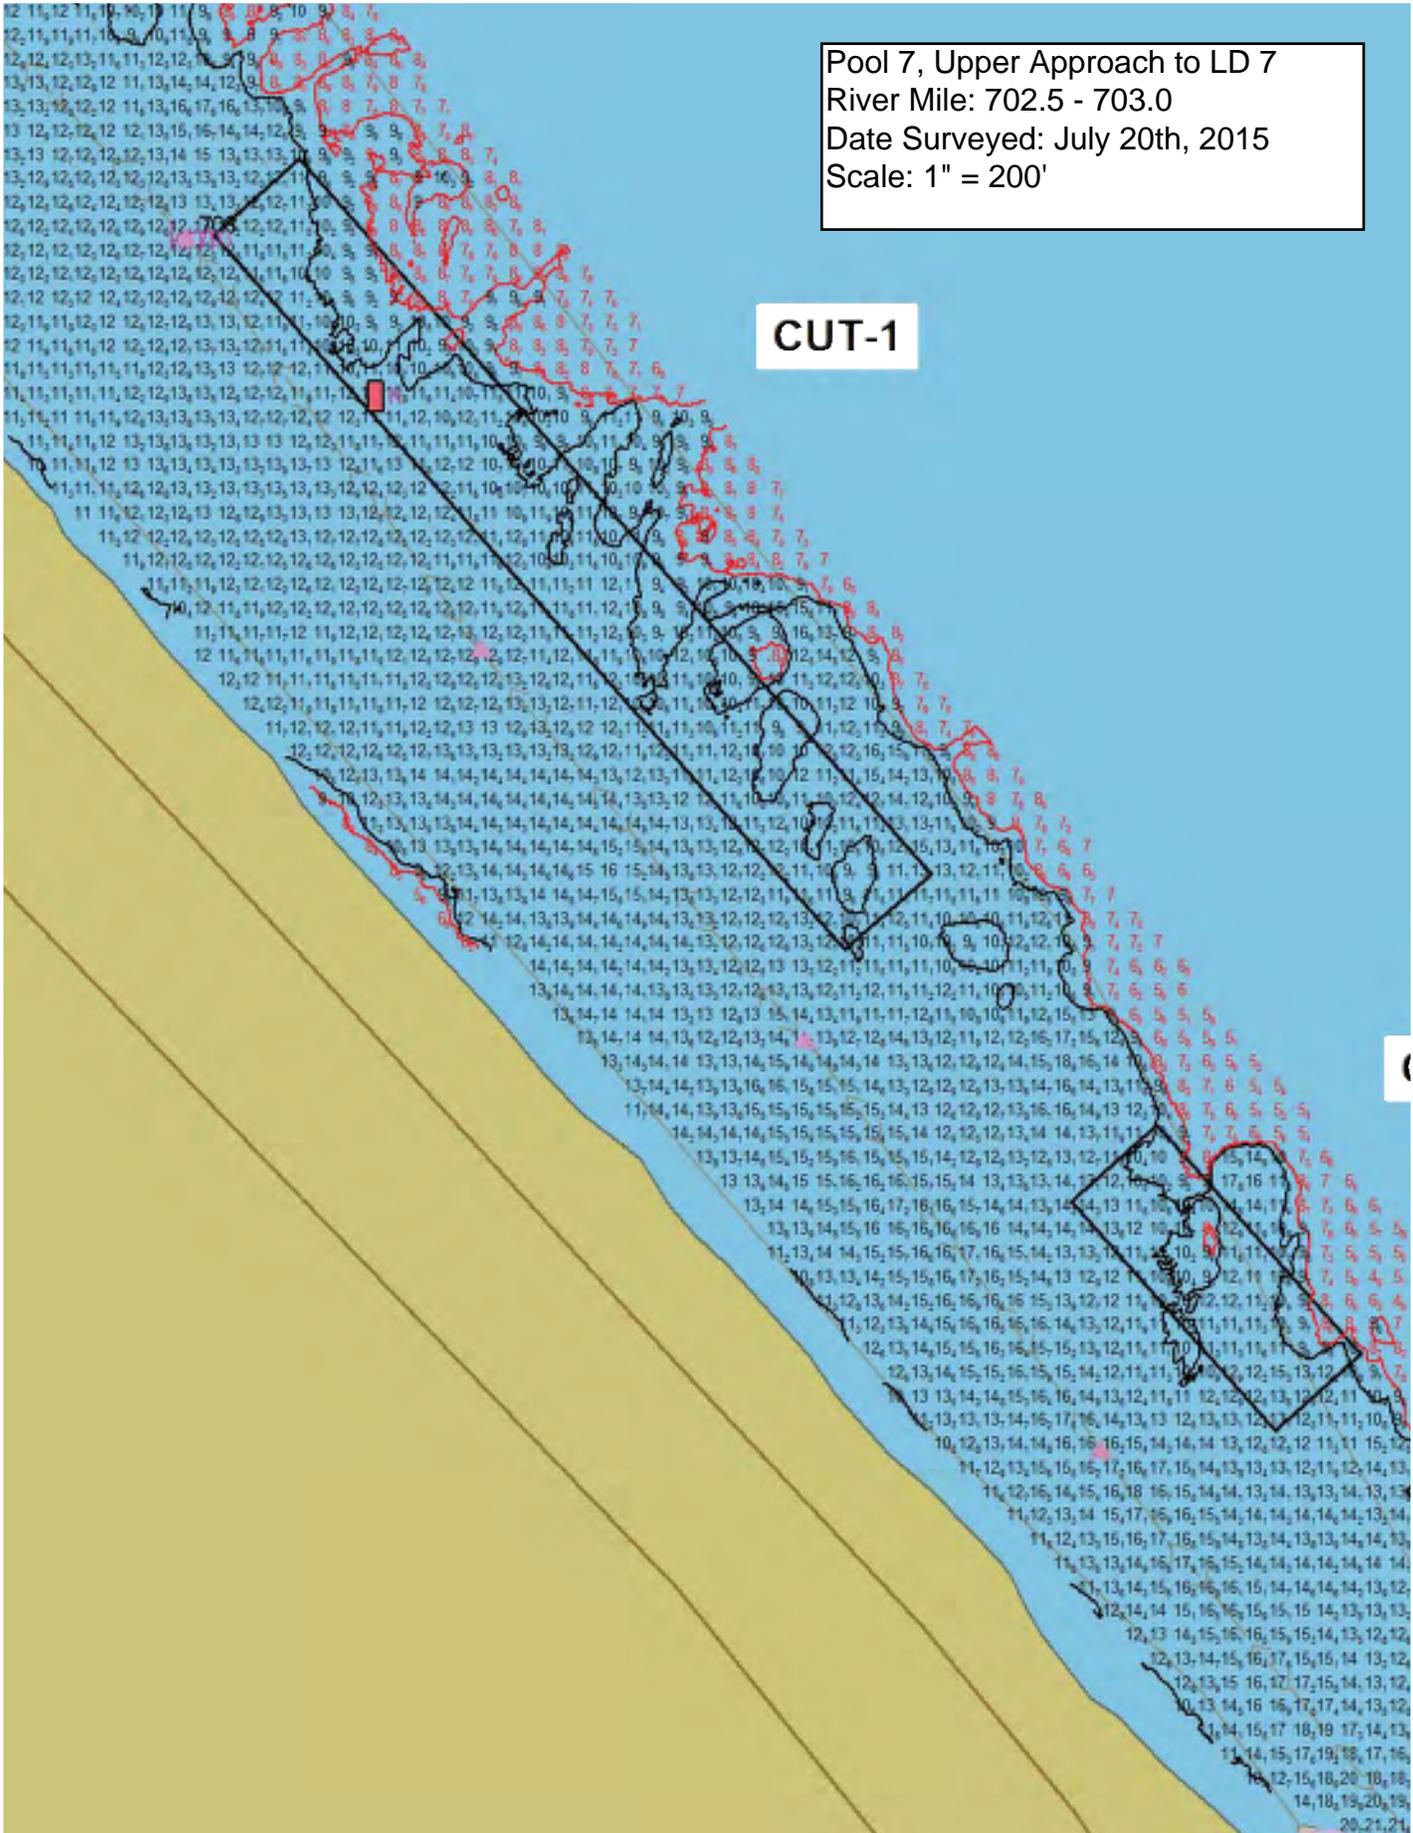

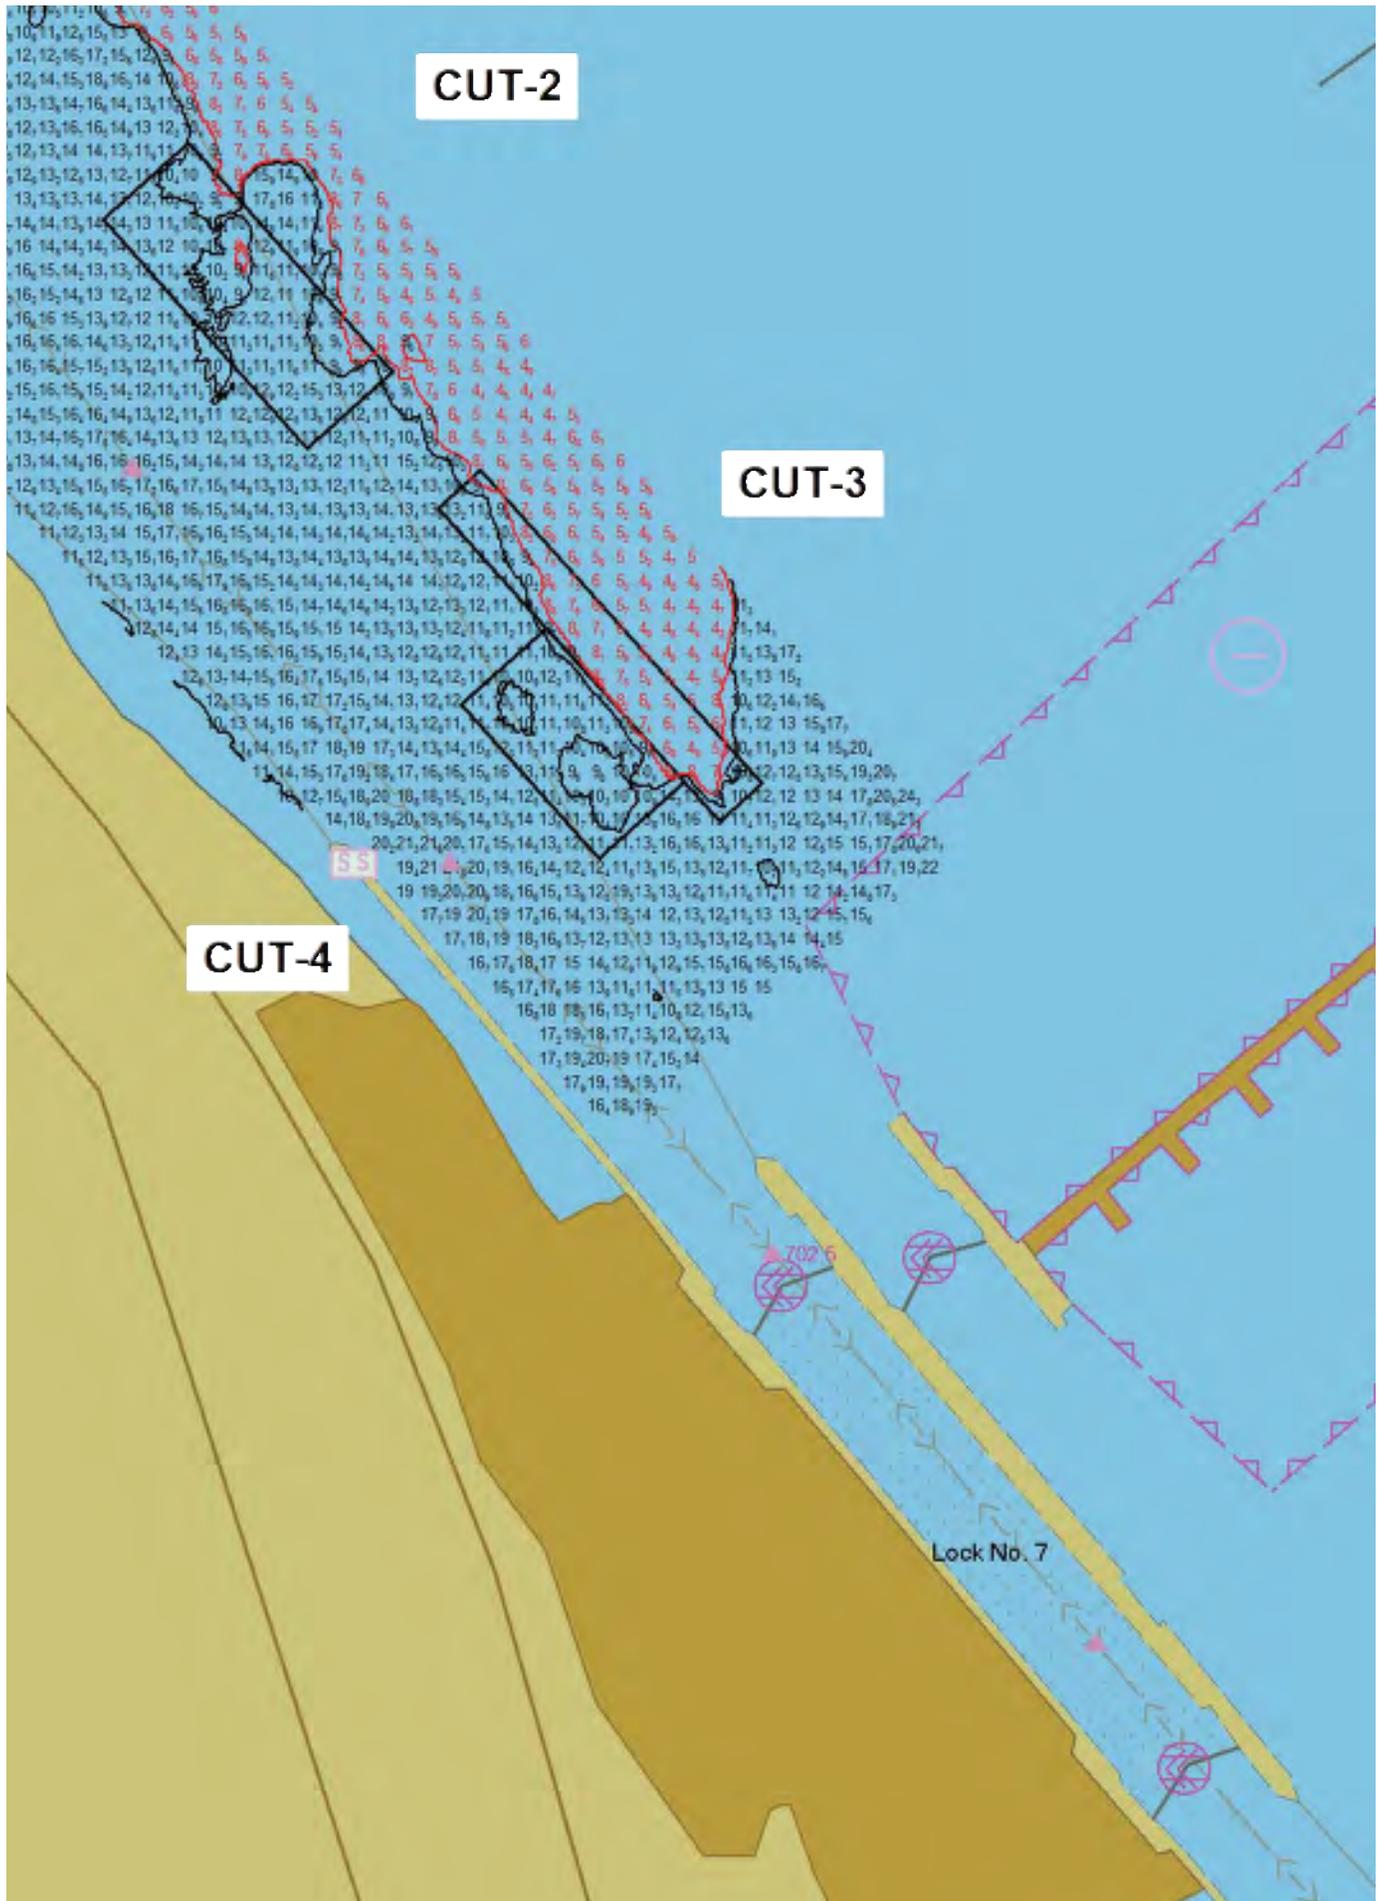

CUT-2

CUT-3

CUT-4

Lock No. 7
