

DN 07-25

DREDGING NOTICE  
U.S. ARMY CORPS OF ENGINEERS  
ST. PAUL DISTRICT

NOTICE DATE: 10 October 2007

DREDGING CATEGORY: Imminent Closure

MEETING DATE: If requested

MEETING TIME:

BOAT REQUIREMENT:

MEETING LOCATION:

---

DREDGE CUT NAME: Indian Camp Light

RIVER MILE: 665.5-665.8

HISTORIC DATA

Frequency: 68%

Avg. Quantity/Job: 26,134 yd<sup>3</sup>

Year Last Dredged: 2006

Avg. Quantity/Year: 17,658 yd<sup>3</sup>

SURVEY DATA

Date Surveyed: 28 June 2007

Water Surface Elevation: 620.4

Low Control Pool Elevation: 620.0

Net Difference: +0.4

5 Day River Forecast: Slow Rise

DREDGING DATA

Recommended Channel Width: 300 feet

Recommended Dredging Depth: 12 feet

Estimated Quantity: 8,483 yd<sup>3</sup>

Type of Dredge: Cont./Mech.

Proposed Dredging Date: 16 October 2007

Estimated Duration: 4 days

Justification for Dredging: The navigation channel is restricted to 140 feet between the 10.5 foot contours and 280 feet between the 9.0 foot contours.

MATERIAL PLACEMENT DATA

Proposed Placement Site: Lansing Hwy. Bridge

Location: 9-663.5-LWP


Site Characteristics: This is a historically used beneficial use stockpile site. All material is expected to be removed.

If you have any questions concerning this project or request an on-site meeting please call me at (608) 687-3112.


Bill Meier  
Acting Channel Maintenance Coordinator

WISCONSIN

### Indian Camp Cut 2

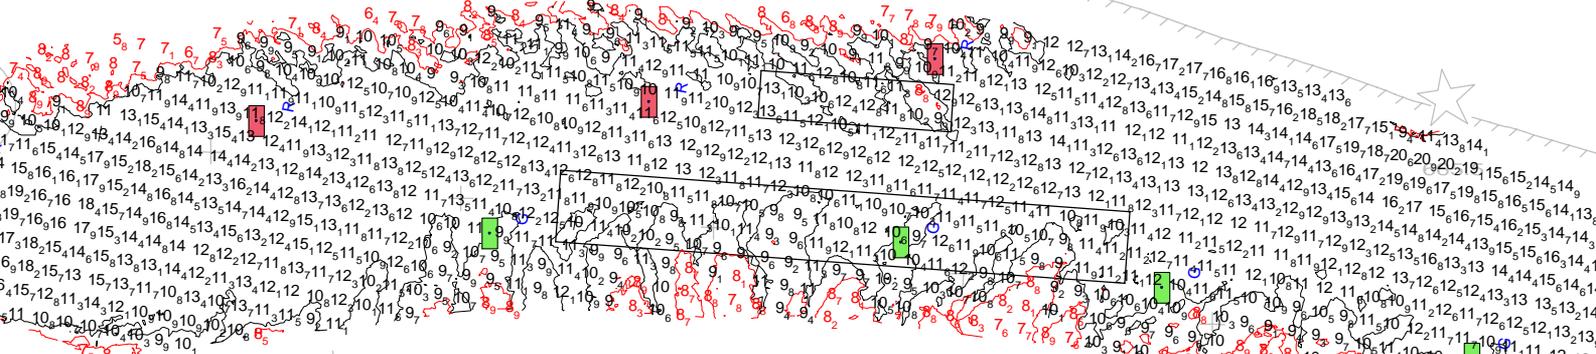

### Indian Camp Cut 1



Pool 9, Indian Camp Light, RM 665.5 - 665.8  
Survey Date: 28 June 2007
