

DN 08-26

DREDGING NOTICE  
U.S. ARMY CORPS OF ENGINEERS  
ST. PAUL DISTRICT

NOTICE DATE: 17 October 2008

REDGING CATEGORY: Routine

MEETING DATE: If requested

MEETING TIME:

BOAT REQUIREMENT:

MEETING LOCATION:

---

DREDGE CUT NAME: Abv Lowry Ave Bridge

RIVER MILE: 856.4 - 856.9

HISTORIC DATA

Frequency: 58%

Avg. Quantity/Job: 35,958 yd<sup>3</sup>

Year Last Dredged: 2006

Avg. Quantity/Year: 20,818 yd<sup>3</sup>

SURVEY DATA

Date Surveyed: 15 October 2008

Water Surface Elevation: 799.4

Low Control Pool Elevation: 796.5

Net Difference: +2.9

5-Day River Forecast: Holding steady

DREDGING DATA

Recommended Channel Width: 140 feet

Recommended Dredging Depth: 12 feet

Estimated Quantity: 27,618 yd<sup>3</sup>

Type of Dredge: Cont./Mech.

Proposed Dredging Date: 21 October 2008

Estimated Duration: 14 dredging days

Justification for Dredging: The navigation channel is closed between the 10.5 foot and 9.0 foot contours.

MATERIAL PLACEMENT DATA

Proposed Placement Site: USAF Site


Location: U-856.6-RMP

Site Characteristics: This is a historically used stockpile site provided by the City of Minneapolis.

If you have any questions concerning this project or request an on-site meeting, please call me at (608) 687-3112.

Dan Cottrell  
Channel Maintenance Coordinator

NSP RIVERSIDE STATION

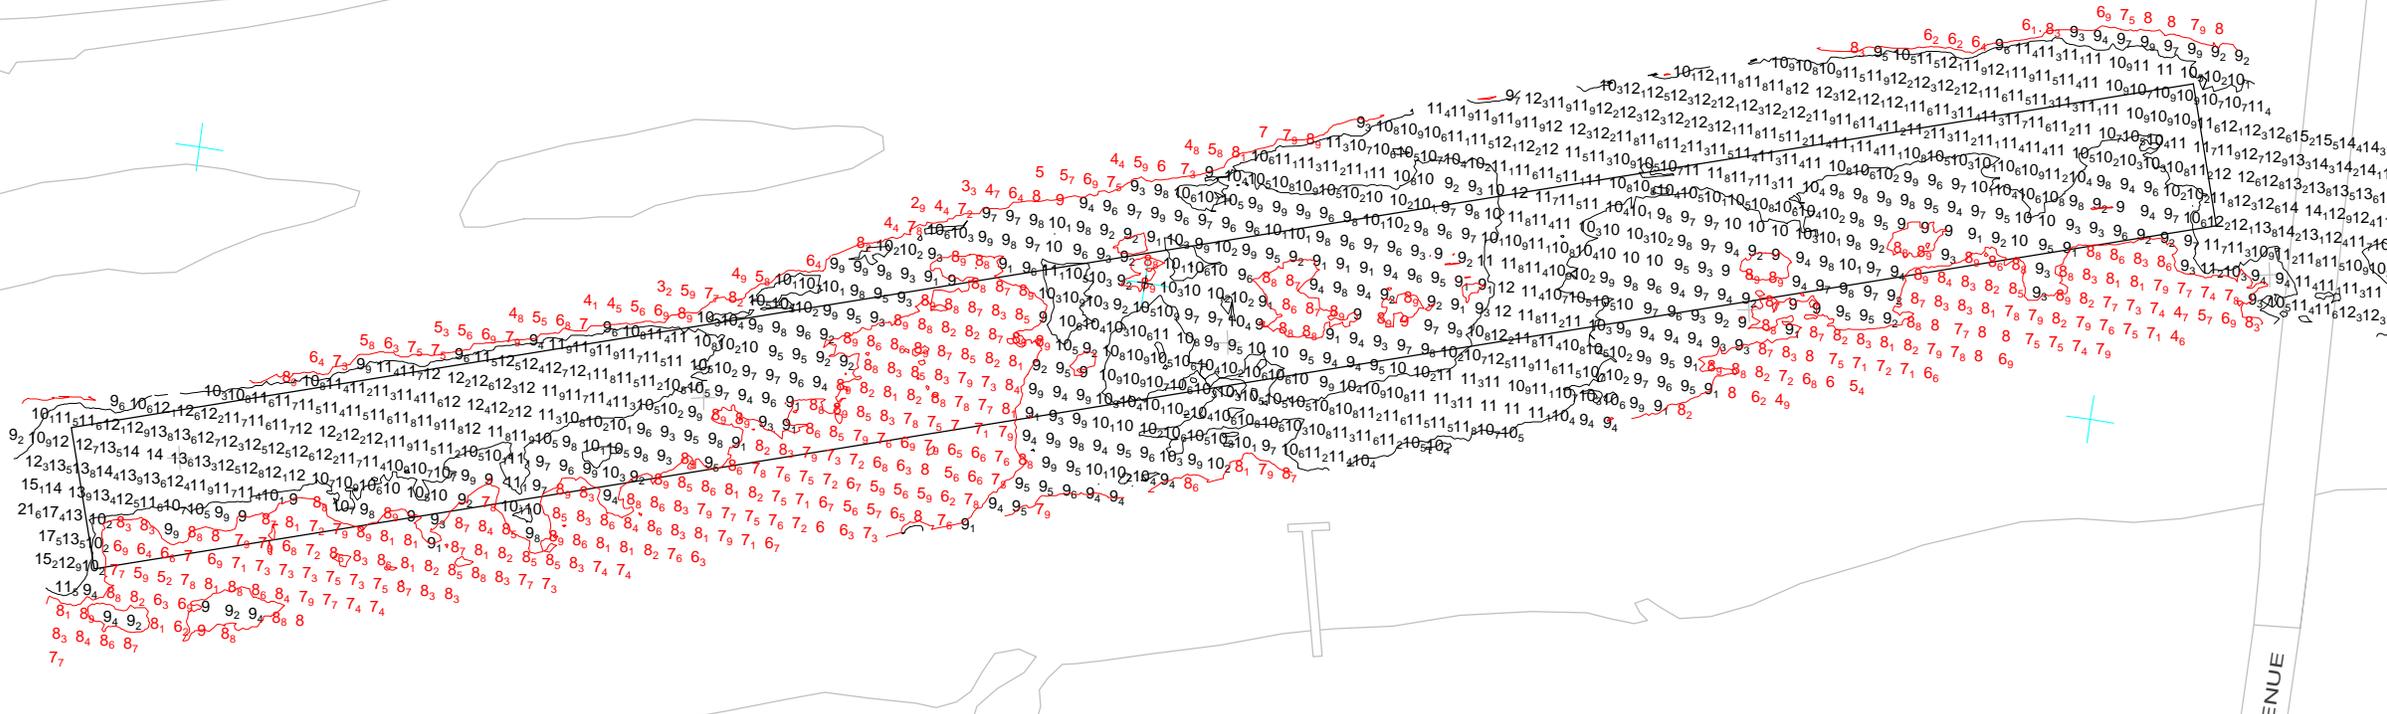

Pool USAF, Abv. Lowry Ave. Br. , RM 856.4 - 856.9  
 Survey Date: 15 October 2008  
 Scale: 1" = 200'  
 To get full survey, print on a legal page 8" X 14"

LOWRY AVENUE

AVENUE
