


Navigation Channel Condition Status Report - St. Paul District

7/9/2025

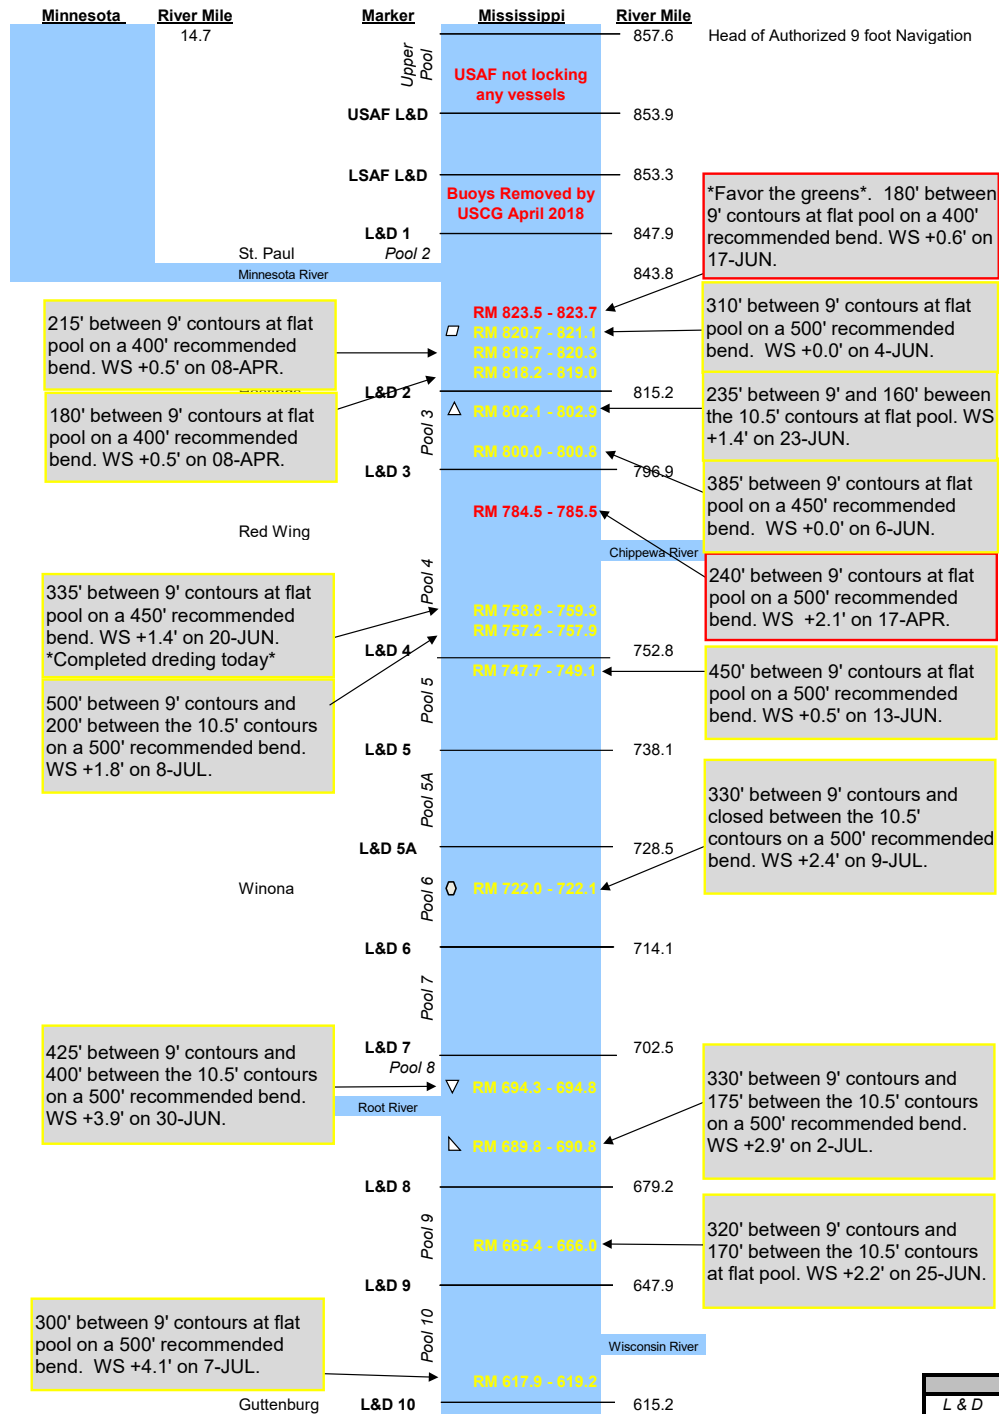

Lock & Dam Status:

Lock 5: NAV Notice 205788, All tows should avoid the last 50' of the lower guide wall due to conditions.

Lock 7: NAV Notice 210767, Lock 7 will be closed to all navigation for four 12-hour closures from 0700 - 1900 on the following days. Tuesday 22 July, Thursday 24 July, Tuesday 29 July and Thursday 31 July.

Lock 9: NAV Notice 14006-1, All tows should avoid the river side and tip of the lower guide wall bullnose, there is potential for exposed steel.

Dredge Status:

Dredge Goetz: Completed dredging at Teepeeota Point on 6 July. Expected to begin dredging at Above Brownsville in Pool 8 tonight. This is expected to be the last job for the St. Paul District before departing for St. Louis District.

Government Mechanical Plant 1: Completed first job at Gravel Point on 8 July. Going to dredge some additional material starting tomorrow 10 July.

Contract Mechanical Plant 1: Began dredging at Sand Slough in Pool 8 on 8 July. Expected to be there until late next week.

Contract Mechanical Plant 2: Expected to be at Morgans Coulee in Pool 3 until mid-July.

IDIQ Unload Contractor - Plant 3: Began unloading in Pool 9 in 8 July.

Island Construction Contractor - Plant 4: Began dredging at Boulanger Bend in Pool 2 on 17 June expected to be there until late July.

Channel Marker Status:

USCG Buoy Tender Sangamon made it to St. Paul on Saturday 31 May they have since exited the District. The next buoy tender run is TBD.

Water Control Status:				
L & D	09-Jul	02-Jul	Gates Pulled	L & D Outdraft Warning
USAF	-	-	N/A	N/A
LSAF	-	-	50,000	20,000
LD 1	NA	NA	N/A	0.2' of flow over rubber dam
LD 2	46,900	44,400	61,000	31,000
LD 3	44,000	44,000	36,000	21,000
LD 4	71,900	79,100	89,000	60,000
LD 5	75,600	87,100	116,000	70,000
LD 5A	83,200	70,800	57,000	32,000
LD 6	73,200	83,200	76,000	44,600
LD 7	74,900	81,400	82,000	44,000
LD 8	82,100	83,300	96,000	40,200
LD 9	91,500	88,200	64,000	55,000
LD 10	108,500	101,500	73,000	47,000

Key:

- Anticipated Dredging Locations; Within the next week
- Groundings; Within the past week
- Dredge Goetz
- Government Mechanical
- Mechanical Dredge Plant 1
- Mechanical Dredge Plant 2
- Mechanical Dredge Plant 3, 4 & 5
- Miscellaneous Dredging
- Use Extreme Caution when in this area
- Use Caution when navigating through area
- Conditions are good - Routine Dredging may occur

Web Information:

For additional Dredge Schedule information, see the link below:
<http://www.mvp.usace.army.mil/Missions/Navigation/Channel-Maintenance/Dredging-Schedule/>

For hydrographic surveys please go to the national eHydro page and navigate to the location:
<https://www.arcgis.com/apps/dashboards/4b8f2ba307684cf597617bf1b6d2f85d>
