


Navigation Channel Condition Status Report - St. Paul District

5/27/2026

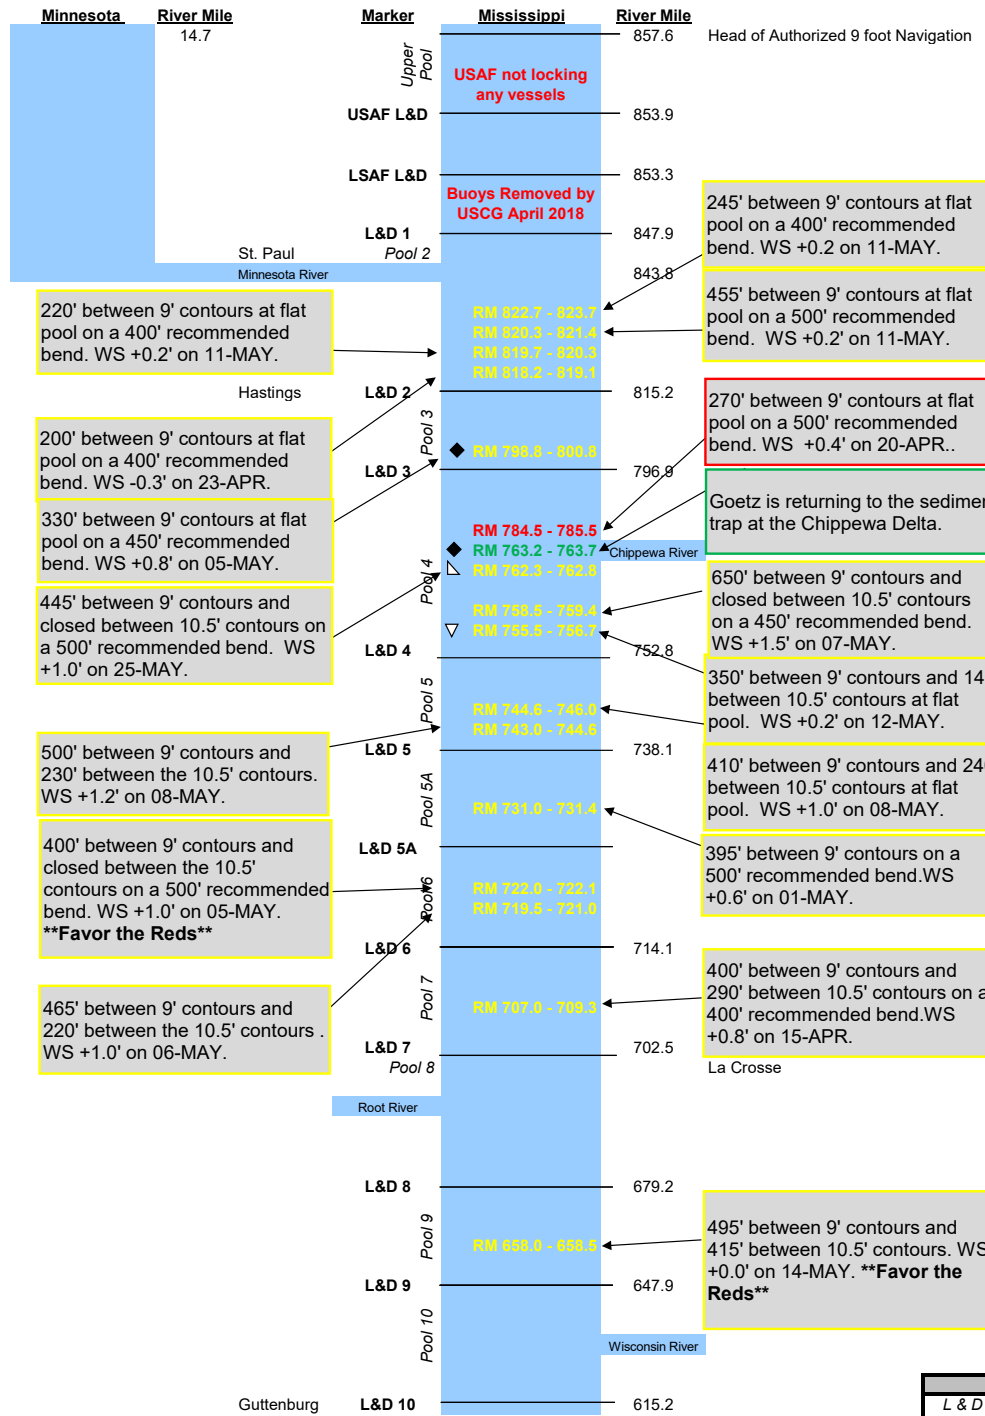

Lock & Dam Status:

Lock 3: NAV Notice 214032, All tows transitioning the lock should stay clear of the quoin on the miter gate #4 the upstream end of the I-wall.

Nav Notice 214090, lock will be closed 28-May 0800 - 1600 hrs.

Lock 5: NAV Notice 205788, All tows should avoid the last 50' of the lower guide wall due to conditions.

Lock 5A: NAV Notice 214031, All tows transitioning the lock should stay clear of the quoin on the miter gate #4 the upstream end of the I-wall.

Lock 7: NAV Notice 211895, Rock weir work on the left descending side of the channel upstream of the lock was completed in late 2025.

Lock 9: NAV Notice 14006-1, All tows should avoid the river side and tip of the lower guide wall bullnose, there is potential for exposed steel.

Dredge Status:

Dredge Goetz: Finished dredging at Chippewa Delta on 25-May, Started dredging at Reads Landing on 26-May. Will return to The Chippewa Delta sediment trap next.

Government Mechanical Plant 1: 2026 start TBD.

Contract Mechanical Plant 1: Began dredging at Grand Encampment in Pool 4 on 22-May. Expected to be there until 15-June.

Contract Mechanical Plant 2: 2026 mobilizing next week to Diamond Bluff in Pool 3.

IDIQ Unload Contractor - Plant 3: 2026 start TBD.

Channel Marker Status:

The USCG Buoy Tender Wyaconda made a complete trip to St Paul and exited the district Sunday 05-April. A USCG Buoy Tender return is TBD. 27-May: No change.

Water Control Status:				
L & D	27-May	20-May	Gates Pulled	L & D Outdraft Warning
USAF	-	-	N/A	N/A
LSAF	-	-	50,000	20,000
LD 1	NA	NA	N/A	0.2' of flow over rubber dam
LD 2	15,600	16,400	61,000	31,000
LD 3	22,100	22,200	36,000	21,000
LD 4	28,900	29,100	89,000	60,000
LD 5	31,100	31,900	116,000	70,000
LD 5A	33,900	34,100	57,000	32,000
LD 6	34,600	34,600	76,000	44,600
LD 7	34,200	34,500	82,000	44,000
LD 8	41,100	36,300	96,000	40,200
LD 9	39,900	34,300	64,000	55,000
LD 10	51,600	47,800	73,000	47,000

Key:

- ◆ Anticipated Dredging Locations; Within the next week
- ☆ Groundings; Within the past week
- △ Dredge Goetz
- Government Mechanical
- ▽ Mechanical Dredge Plant 1
- △ Mechanical Dredge Plant 2
- Mechanical Dredge Plant 3, 4 & 5
- Miscellaneous Dredging
- Red Box Use Extreme Caution when in this area
- Yellow Box Use Caution when navigating through area
- Green Box Conditions are good - Routine Dredging may occur

Web Information:

For additional Dredge Schedule information, see the link below:
<http://www.mvp.usace.army.mil/Missions/Navigation/Channel-Maintenance/Dredging-Schedule/>

For hydrographic surveys please go to the national eHydro page and navigate to the location:
<https://www.arcgis.com/apps/dashboards/4b8f2ba307684cf597617bf1b6d2f85d>
