


## Navigation Channel Condition Status Report - St. Paul District 2026-06-10

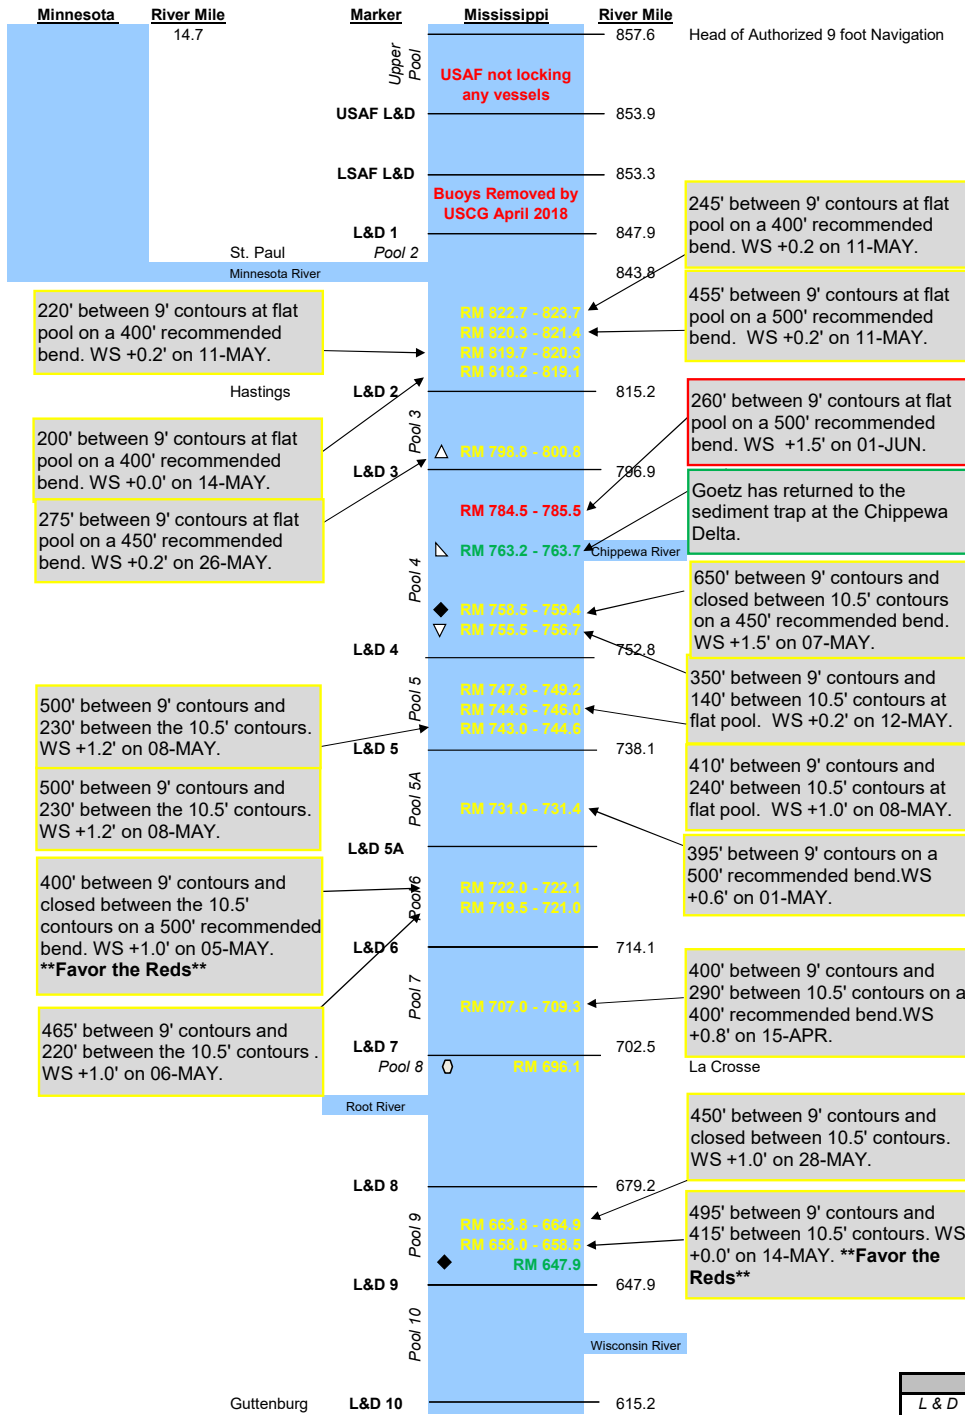

**Lock & Dam Status:**

**Lock 3:** NAV Notice 214032, All tows transitioning the lock should stay clear of the quoin on the miter gate #4 the upstream end of the I-wall.

**Lock 5:** NAV Notice 205788, All tows should avoid the last 50' of the lower guide wall due to conditions.

**Lock 5A:** NAV Notice 214031, All tows transitioning the lock should stay clear of the quoin on the miter gate #4 the upstream end of the I-wall.

**Lock 7:** NAV Notice 211895, Rock weir work on the left descending side of the channel upstream of the lock was completed in late 2025.

**Lock 9:** NAV Notice 14006-1, All tows should avoid the river side and tip of the lower guide wall bullnose, there is potential for exposed steel.

**Dredge Status:**

**Dredge Goetz:** Began dredging at Chippewa Delta in lower Pool 4 again on 01-June, expected to be there until 16-June.

**Government Mechanical Plant 1:** Began Dredging at Isle La Plume access in Pool 8 on 10-June. Will be going to LD 9 Aux Chamber next.

**Contract Mechanical Plant 1:** Began dredging at Grand Encampment in Pool 4 on 22-May. Expected to be there until 16-June.

**Contract Mechanical Plant 2:** Began dredging at Diamond Bluff in Pool 3 on 02-June. Expected to be there until 2-July.

**IDIQ Unload Contractor - Plant 3:** 2026 start TBD.

**Channel Marker Status:**

The USCG Buoy Tender Wyaconda made a complete trip to St Paul and exited the district Sunday 05-April. A USCG Buoy Tender return is TBD. 10-June: No change.

Water Control Status:				
L & D	10-Jun	03-Jun	Gates Pulled	L & D Outdraft Warning
USAF	-	-	N/A	N/A
LSAF	-	-	50,000	20,000
LD 1	NA	NA	N/A	0.2' of flow over rubber dam
LD 2	12,100	11,400	61,000	31,000
LD 3	15,100	18,100	36,000	21,000
LD 4	18,600	21,900	89,000	60,000
LD 5	19,600	25,300	116,000	70,000
LD 5A	22,600	28,800	57,000	32,000
LD 6	23,300	28,900	76,000	44,600
LD 7	23,800	29,500	82,000	44,000
LD 8	27,400	32,100	96,000	40,200
LD 9	27,700	30,900	64,000	55,000
LD 10	37,400	40,300	73,000	47,000

**Key:**

- ◆ Anticipated Dredging Locations; Within the next week
- ☆ Groundings; Within the past week
- △ Dredge Goetz
- Government Mechanical
- ▽ Mechanical Dredge Plant 1
- △ Mechanical Dredge Plant 2
- Mechanical Dredge Plant 3, 4 & 5
- Miscellaneous Dredging
- Use Extreme Caution when in this area
- Use Caution when navigating through area
- Conditions are good - Routine Dredging may occur

**Web Information:**

For additional Dredge Schedule information, see the link below:  
<http://www.mvp.usace.army.mil/Missions/Navigation/Channel-Maintenance/Dredging-Schedule/>

For hydrographic surveys please go to the national eHydro page and navigate to the location:  
<https://www.arcgis.com/apps/dashboards/4b8f2ba307684cf597617bf1b6d2f85d>
