

DREDGING NOTICE  
U.S. ARMY CORPS OF ENGINEERS  
ST. PAUL DISTRICT

NOTICE DATE: August 1st, 2024	DREDGING CATEGORY: Imminent
MEETING DATE: If requested	MEETING TIME:
BOAT REQUIREMENT:	MEETING LOCATION:
DREDGE CUT NAME: Coulters Island	RIVER MILE: 801.4 – 802.0

**HISTORIC DATA**

Frequency: 55%	Avg. Quantity/Job: 26,755 yd <sup>3</sup>
Date Last Dredged: Aug 22 <sup>nd</sup> , 2025	Avg. Quantity/Year: 14,594 yd <sup>3</sup>

**SURVEY DATA**

Date Surveyed: June 3<sup>rd</sup>, 2025  
Water Surface Elevation: 674.3  
Low Control Pool Elevation: 673.9  
Net Difference: +0.4  
5-Day River Forecast: currently decreasing then leveling out

**DREDGING DATA**


Recommended Channel Width: 300 feet  
Recommended Dredging Depth: 12 feet  
Estimated Quantity: 30,957 yd<sup>3</sup>  
Type of Dredge: Contract Mechanical Plant 2  
Proposed Dredging Date: June 5<sup>th</sup>, 2025  
Estimated Duration: 15 dredging days  
Justification for Dredging: The navigation channel is reduced to 240' between the 9.0' contours and 80' between the 10.5' contours.

**MATERIAL PLACEMENT DATA**

Proposed Placement Site: Corps Island  
Location: 3-799.2-RMT  
Site Characteristics: This is a historically used transfer site.

If you have any questions concerning this project or if you would like to request an on-site meeting, please call me at (651) 350-2564.

Eric Hammer  
Channel Maintenance Coordinator

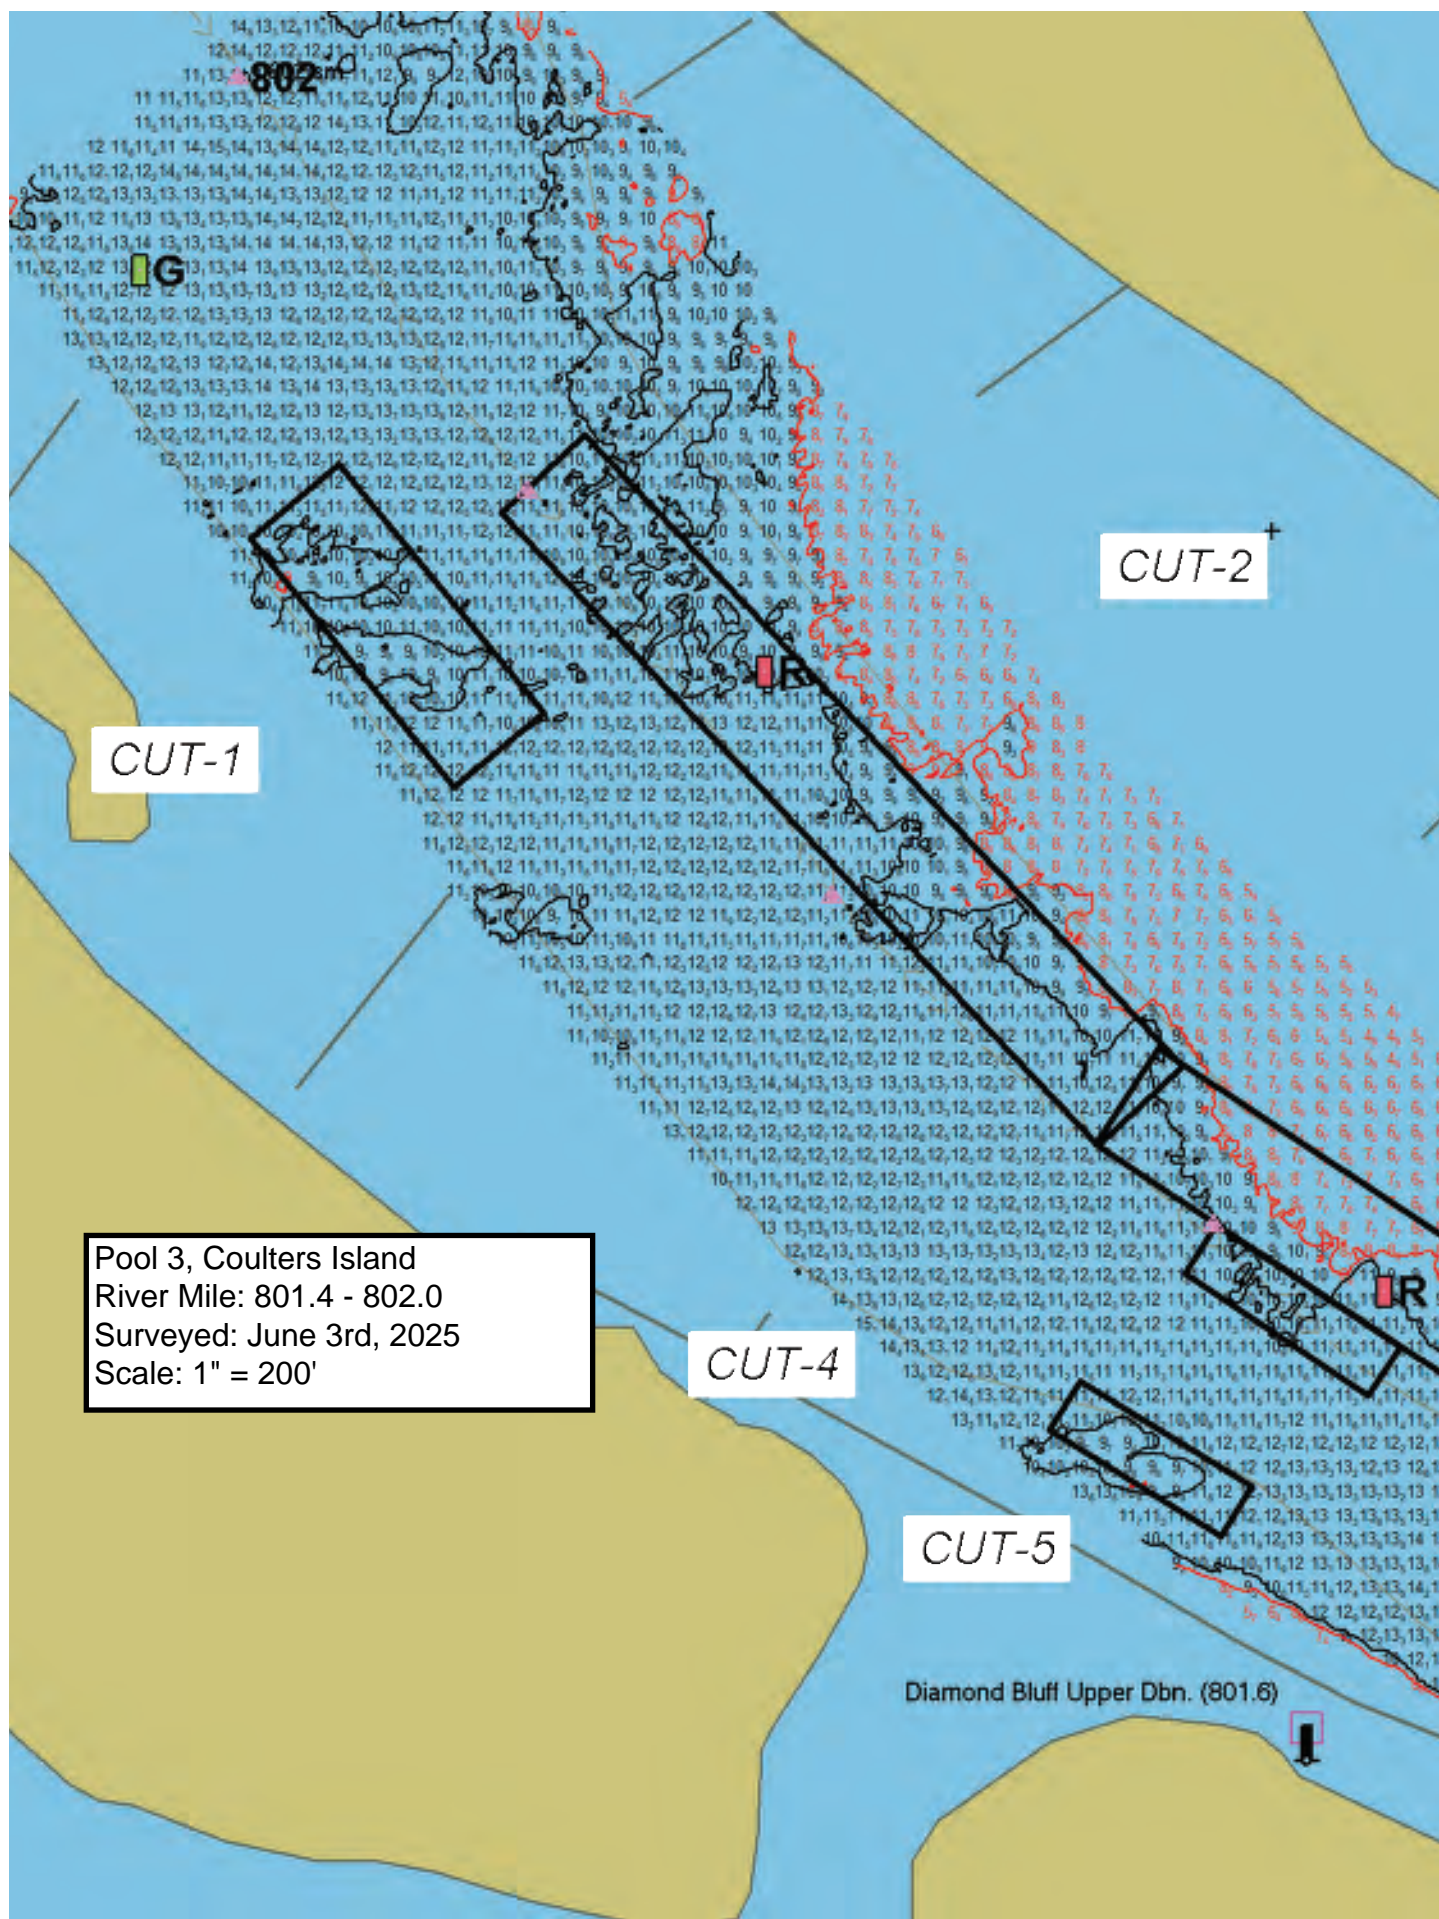



CUT-3

CUT-6

Upper Dbn. (801.6)

801.5
