

DN 22-09

DREDGING NOTICE
U.S. ARMY CORPS OF ENGINEERS
ST. PAUL DISTRICT

NOTICE DATE: June 15th, 2022

DREDGING CATEGORY: Imminent

MEETING DATE: If requested

MEETING TIME:

BOAT REQUIREMENT:

MEETING LOCATION:

DREDGE CUT NAME: Grand Encampment

RIVER MILE: 756.2 – 756.8

HISTORIC DATA

Frequency: 69%

Avg. Quantity/Job: 47,039 yd³

Date Last Dredged: Oct. 18th, 2021

Avg. Quantity/Year: 32,565 yd³

SURVEY DATA

Date Surveyed: June 9th, 2022

Water Surface Elevation: 667.5

Low Control Pool Elevation: 666.3

Net Difference: +1.2'

5 Day River Forecast: Holding Steady

DREDGING DATA

Recommended Channel Width: 300 feet

Recommended Dredging Depth: 12 feet

Estimated Quantity: 27,988 yd³

Type of Dredge: Government Mechanical

Proposed Dredging Date: June 16th, 2022

Estimated Duration: 19 dredging days

Justification for Dredging: The navigation channel is reduced to 210' between the 9' contours and closed between the 10.5' contours.

MATERIAL PLACEMENT DATA


Proposed Placement Site: Teepeeota Point

Location: 4-757.5-LWT

Site Characteristics: This is a historically used temporary island site.

If you have any questions concerning this project, or if you would like to request an on-site meeting, please call me at (651) 290-5155.

Dan Cottrell
Dredging Manager

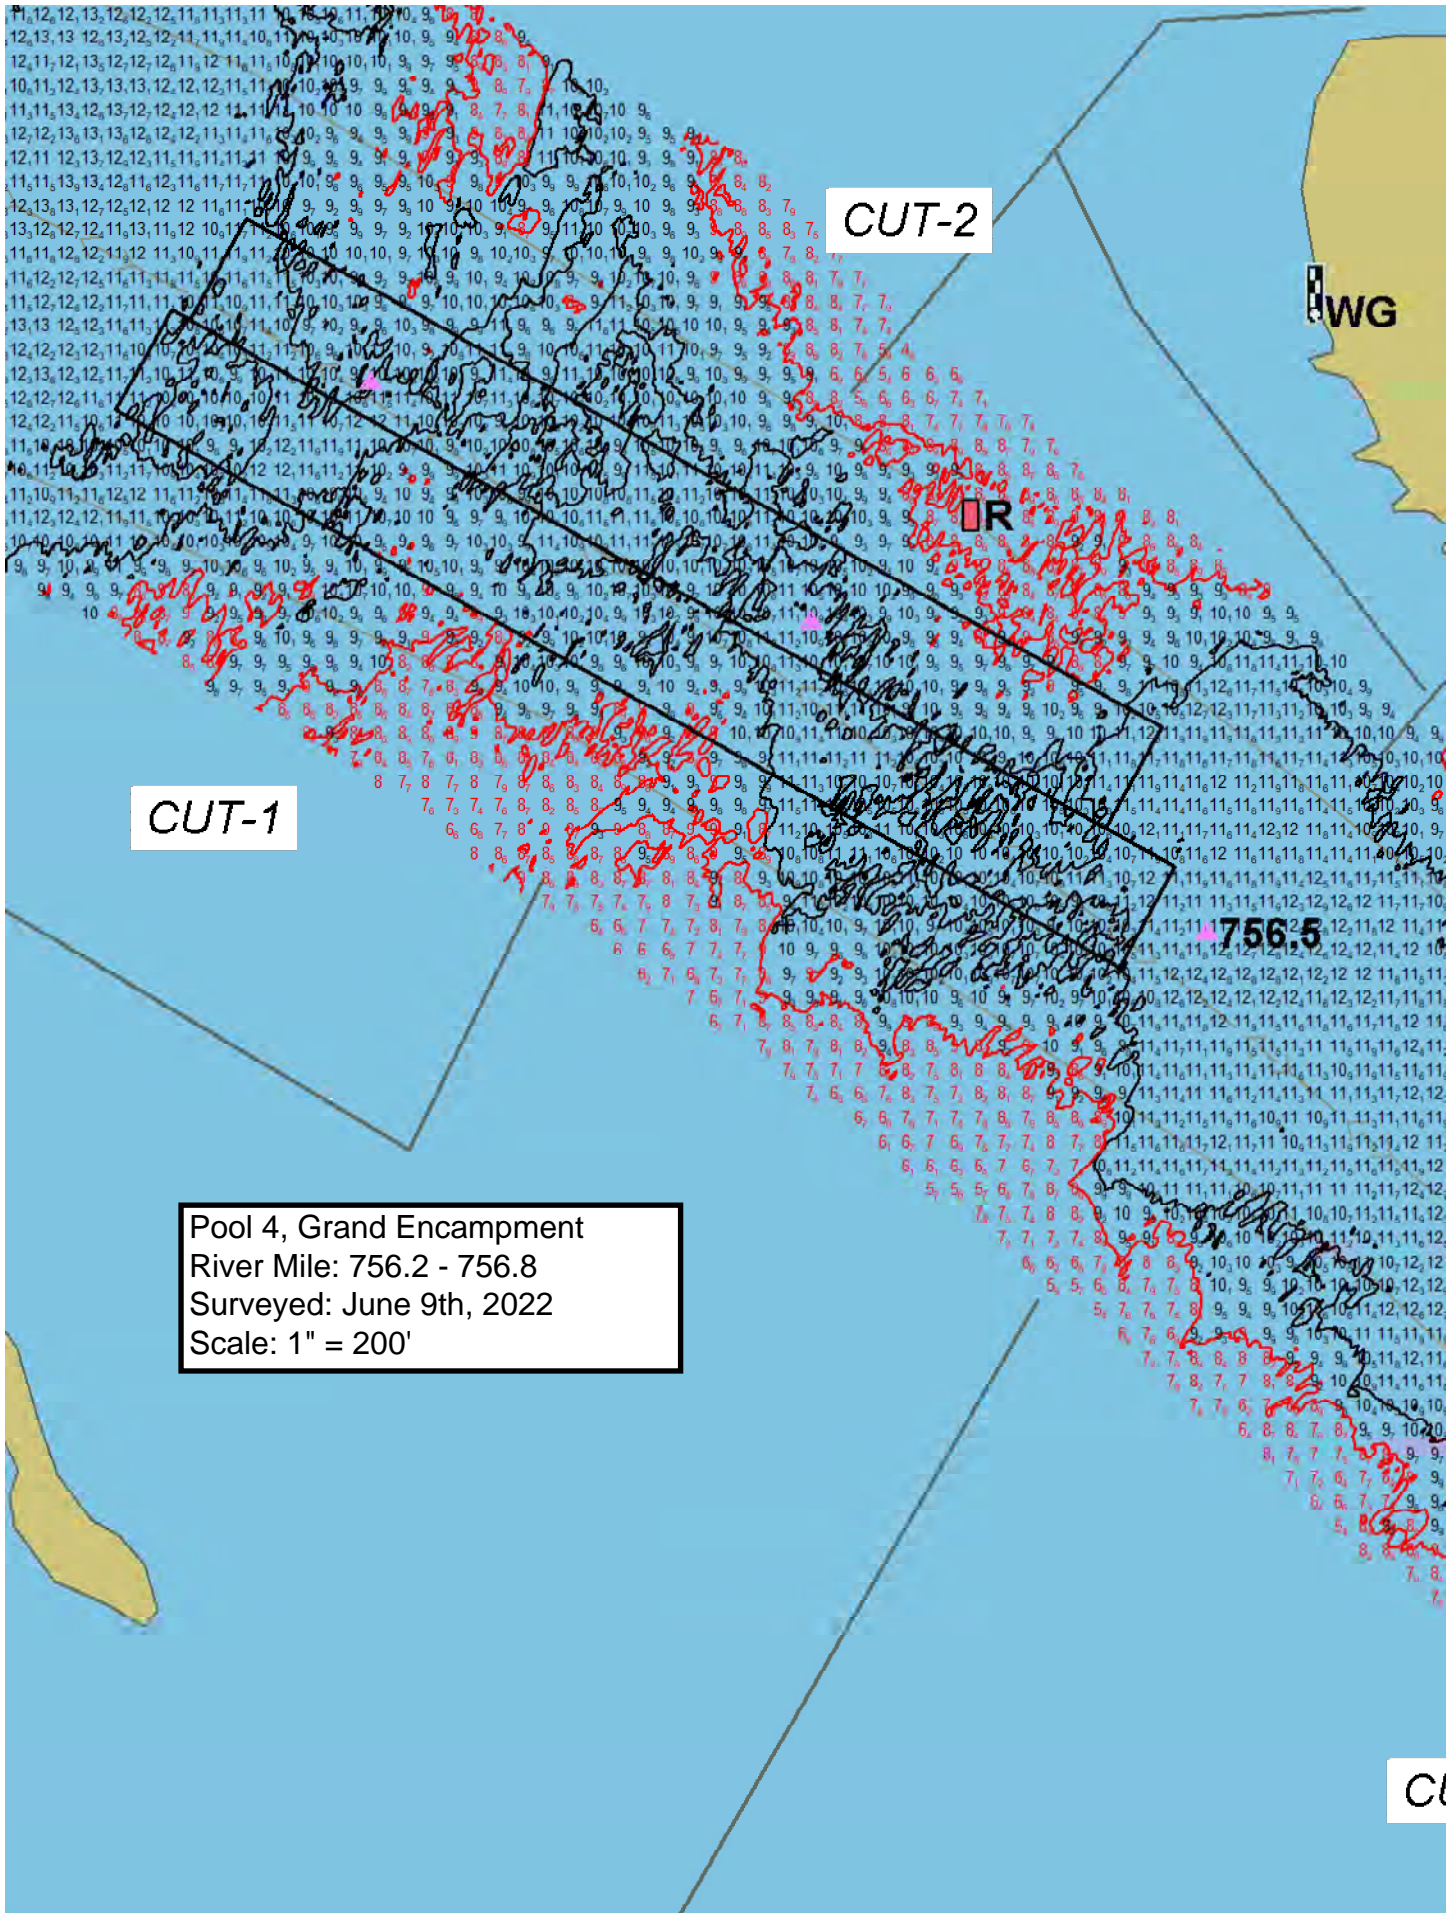

CUT-2

WG


IR

CUT-1

756.5

Pool 4, Grand Encampment
River Mile: 756.2 - 756.8
Surveyed: June 9th, 2022
Scale: 1" = 200'

CL

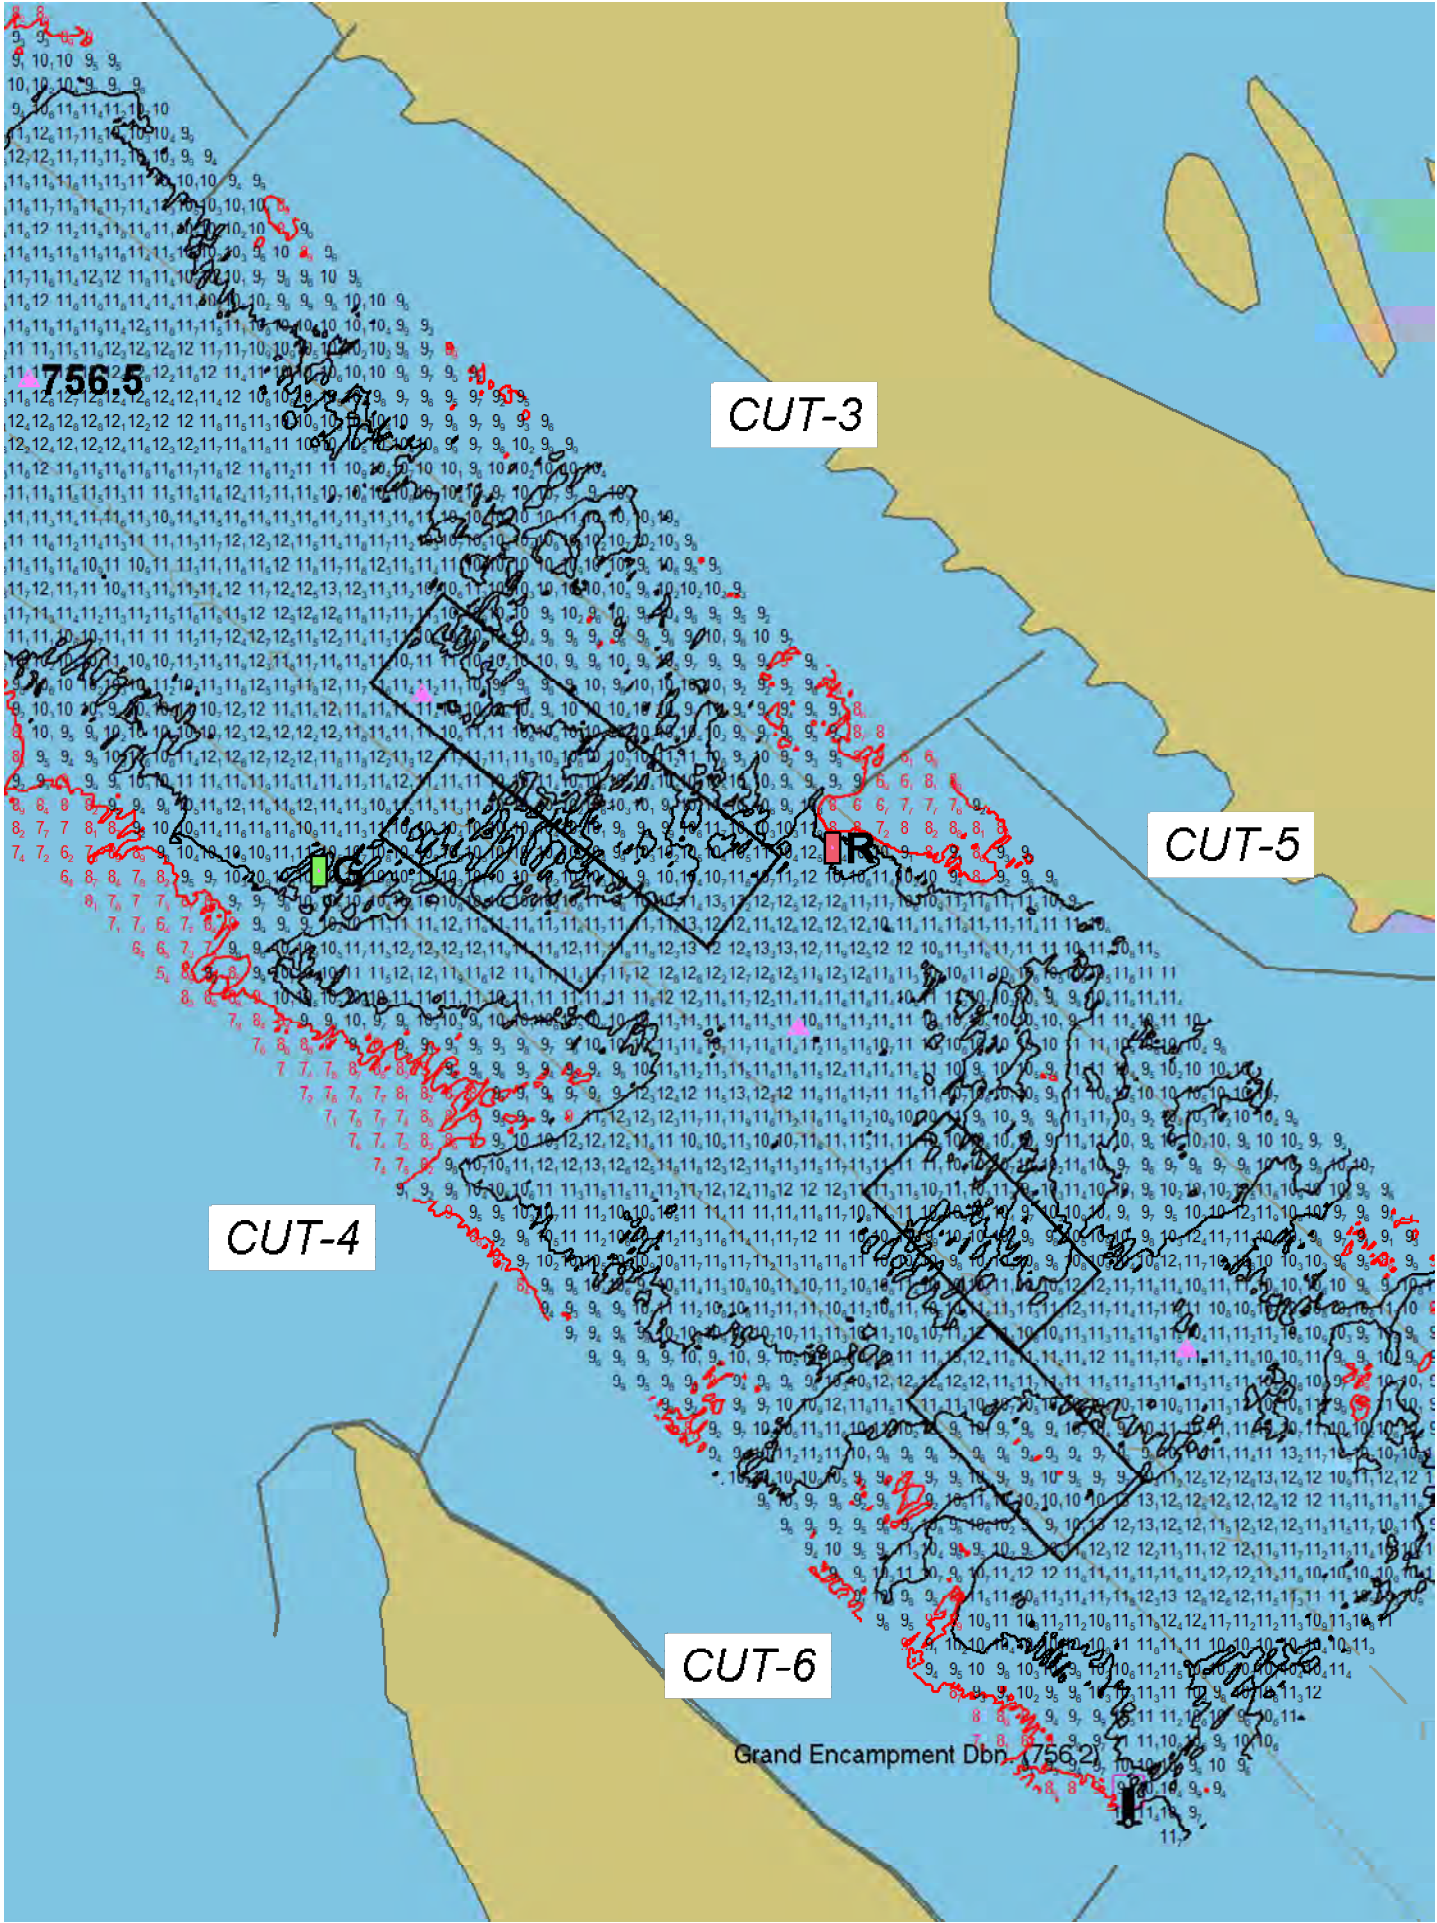

CUT-3

CUT-5

CUT-4

CUT-6

7565

Grand Encampment Dbn (7562)

11,
