

DREDGING NOTICE
U.S. ARMY CORPS OF ENGINEERS
ST. PAUL DISTRICT

NOTICE DATE: August 2 nd , 2019	DREDGING CATEGORY: Imminent
MEETING DATE: If requested	MEETING TIME:
BOAT REQUIREMENT:	MEETING LOCATION:
DREDGE CUT NAME: Cannon River	RIVER MILE: 792.8 – 793.7

HISTORIC DATA

Frequency: 33 %	Avg. Quantity/Job: 31,582 yd ³
Date Last Dredged: October 10 th , 2018	Avg. Quantity/Year: 10,312 yd ³

SURVEY DATA

Date Surveyed: August 1st, 2019
Water Surface Elevation: 672.1
Low Control Pool Elevation: 666.6
Net Difference: +5.5
5-Day River Forecast: Steady decline

DREDGING DATA


Recommended Channel Width: 300 feet
Recommended Dredging Depth: 11 feet channel
Estimated Quantity: 52,985 yd³ plus 2,382 yd³ for placement site access
Type of Dredge: Contract Mechanical
Proposed Dredging Date: August 26th, 2019
Estimated Duration: 25 – 12 hour dredging days
Justification for Dredging: The navigation channel is closed between the 9.0' contours and 10.5' contours.

MATERIAL PLACEMENT DATA

Proposed Placement Site: Red Wing Commercial Harbor
Location: 4-791.6-RMP
Site Characteristics: This is a historically used upland placement site owned by the City of Red Wing.

If you have any questions concerning this project, or if you would like to request an on-site meeting, please call me at 651-290-5155.

Dan Cottrell
Dredging Manager

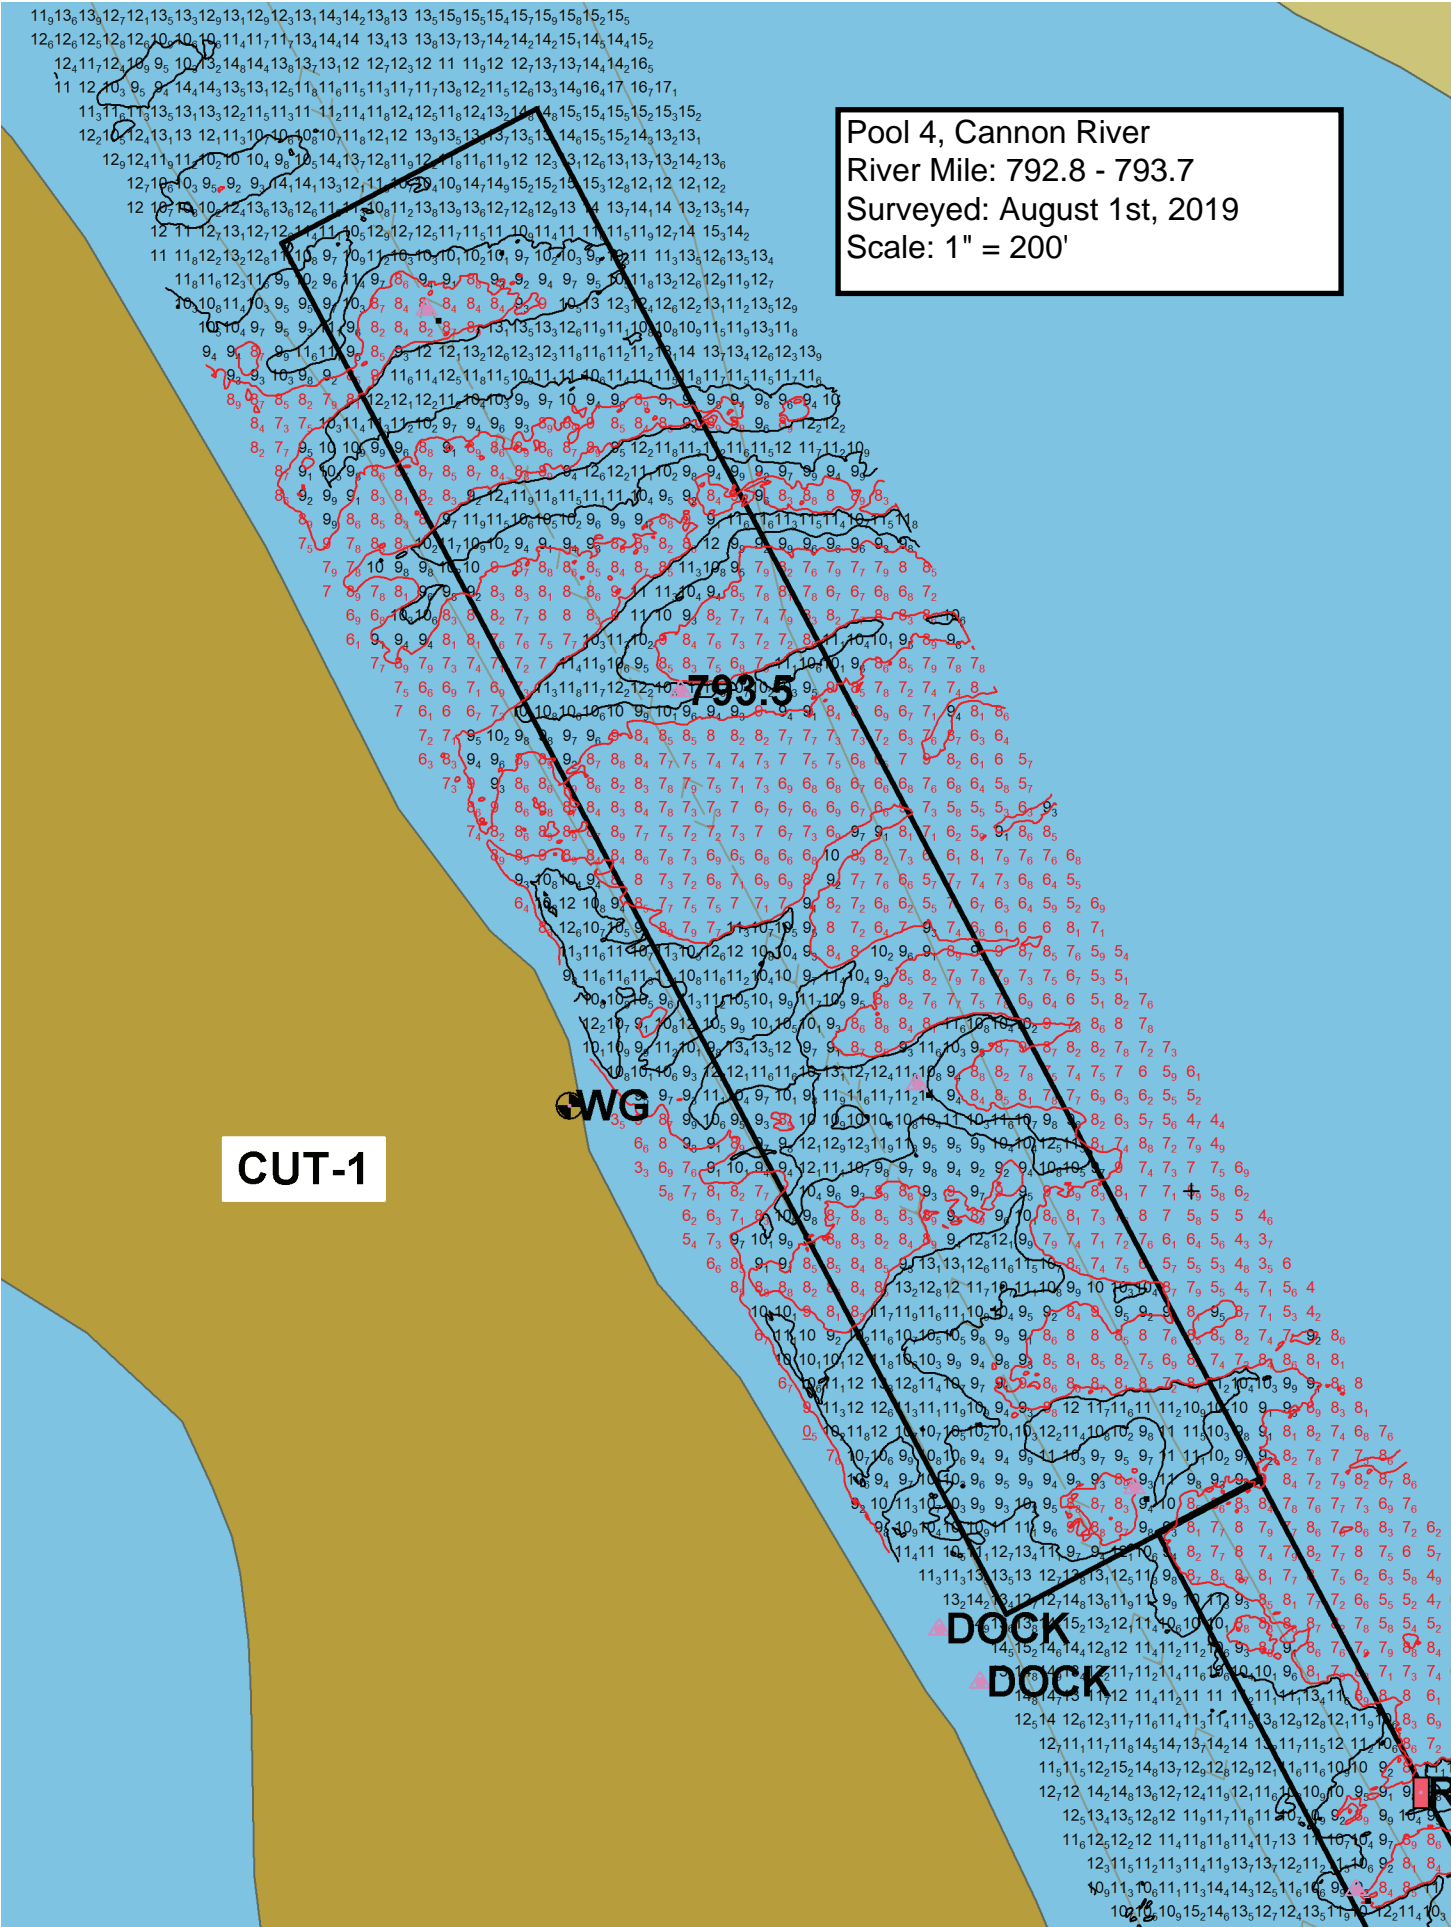

Pool 4, Cannon River
River Mile: 792.8 - 793.7
Surveyed: August 1st, 2019
Scale: 1" = 200'

CUT-1

CWG

DOCK
DOCK

