

DN 06-31

DREDGING NOTICE
U.S. ARMY CORPS OF ENGINEERS
ST. PAUL DISTRICT

NOTICE DATE: 25 September 2006	DREDGING CATEGORY: Routine
MEETING DATE: If requested	MEETING TIME:
BOAT REQUIREMENT:	MEETING LOCATION:
<hr/>	
DREDGE CUT NAME: Blackhawk Park Access	RIVER MILE: 714.1

HISTORIC DATA

Frequency: NA	Avg. Quantity/Job: NA
Year Last Dredged: NA	Avg. Quantity/Year: NA

NOTE: Minor dredging for access to Blackhawk Park has occurred in the past, however it was in association with material placement from another cut and the quantities were insignificant.

SURVEY DATA

Date Surveyed: 15 June 2006
Water Surface Elevation: 621.5
Low Control Pool Elevation: 620.0
Net Difference: 1.5'
5 Day River Forecast: Recede slowly

DREDGING DATA

Recommended Channel Width: 100 feet
Recommended Dredging Depth: 8 feet
Estimated Quantity: 4,836 yd³
Type of Dredge: Cont./Mech.
Proposed Dredging Date: 04 October 2006
Estimated Duration: 4 days
Justification for Dredging: Access to Blackhawk Park is needed for placement of dredged material from the Indian Camp Light dredge cuts.

MATERIAL PLACEMENT DATA


Proposed Placement Site: Blackhawk Park
Location: 9-670.5-LWP
Site Characteristics: Blackhawk Park is a historically used beneficial use site.

If you have any questions concerning this project or request an on-site meeting please call me at (608) 687-3112 ext 3.

Paul Machajewski
Channel Manager

Blackhawk Park: RM 670.9
Survey Date: 15 June 2006
Water Surface: +1.5'

North

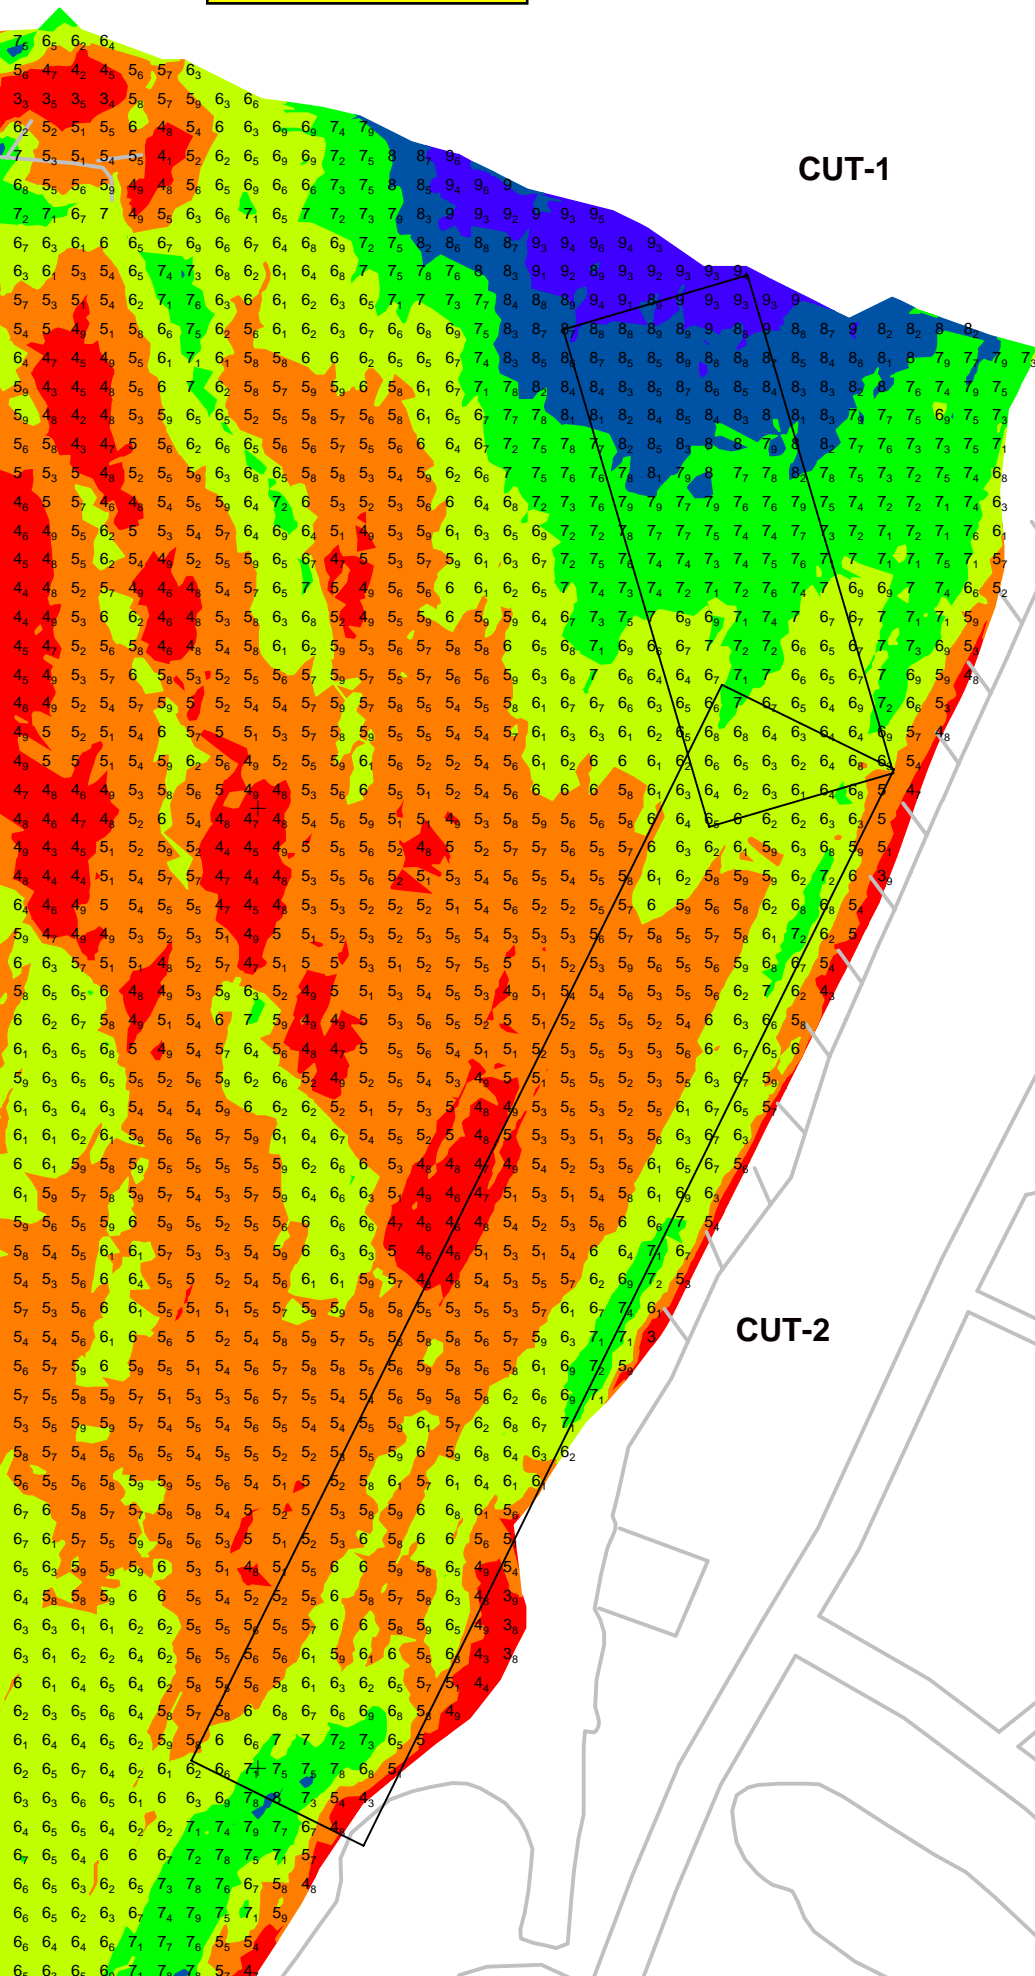

CUT-1

CUT-2

Blackhawk Park
