

DREDGING NOTICE
U.S. ARMY CORPS OF ENGINEERS
ST. PAUL DISTRICT

NOTICE DATE: August 14 th , 2023	DREDGING CATEGORY: Imminent
MEETING DATE: If requested	MEETING TIME:
BOAT REQUIREMENT:	MEETING LOCATION:
DREDGE CUT NAME: Lower Dresbach Island	RIVER MILE: 703.0 - 703.4

HISTORIC DATA

Frequency: 53%	Avg. Quantity/Job: 17,767 yd ³
Date Last Dredged: Sept. 4 th , 2020	Avg. Quantity/Year: 9,386 yd ³

SURVEY DATA

Date Surveyed: August 7th, 2023
Water Surface Elevation: 638.5
Low Control Pool Elevation: 638.5
Net Difference: +0.0'
5 Day River Forecast: No Change

DREDGING DATA


Recommended Channel Width: 300 feet
Recommended Dredging Depth: 13 feet – to try to help with tow boat control
Estimated Quantity: 37,694 yd³ plus 1,406 yd³ for placement site access
Type of Dredge: Contract Mechanical Plant 1
Proposed Dredging Date: August 14th for channel August 11th started access
Estimated Duration: 20 dredging days
Justification for Dredging: The navigation channel is restricted to 275' between the 9.0' contours and 105' between the 10.5' contours.

MATERIAL PLACEMENT DATA

Proposed Placement Site: Dakota Island
Locations: 7-706.5-RMT
Site Characteristics: This is a historically used temporary island placement site.

If you have any questions concerning this project, or if you would like to request an on-site meeting, please call me at (651) 290-5155.

Dan Cottrell
Dredging Manager

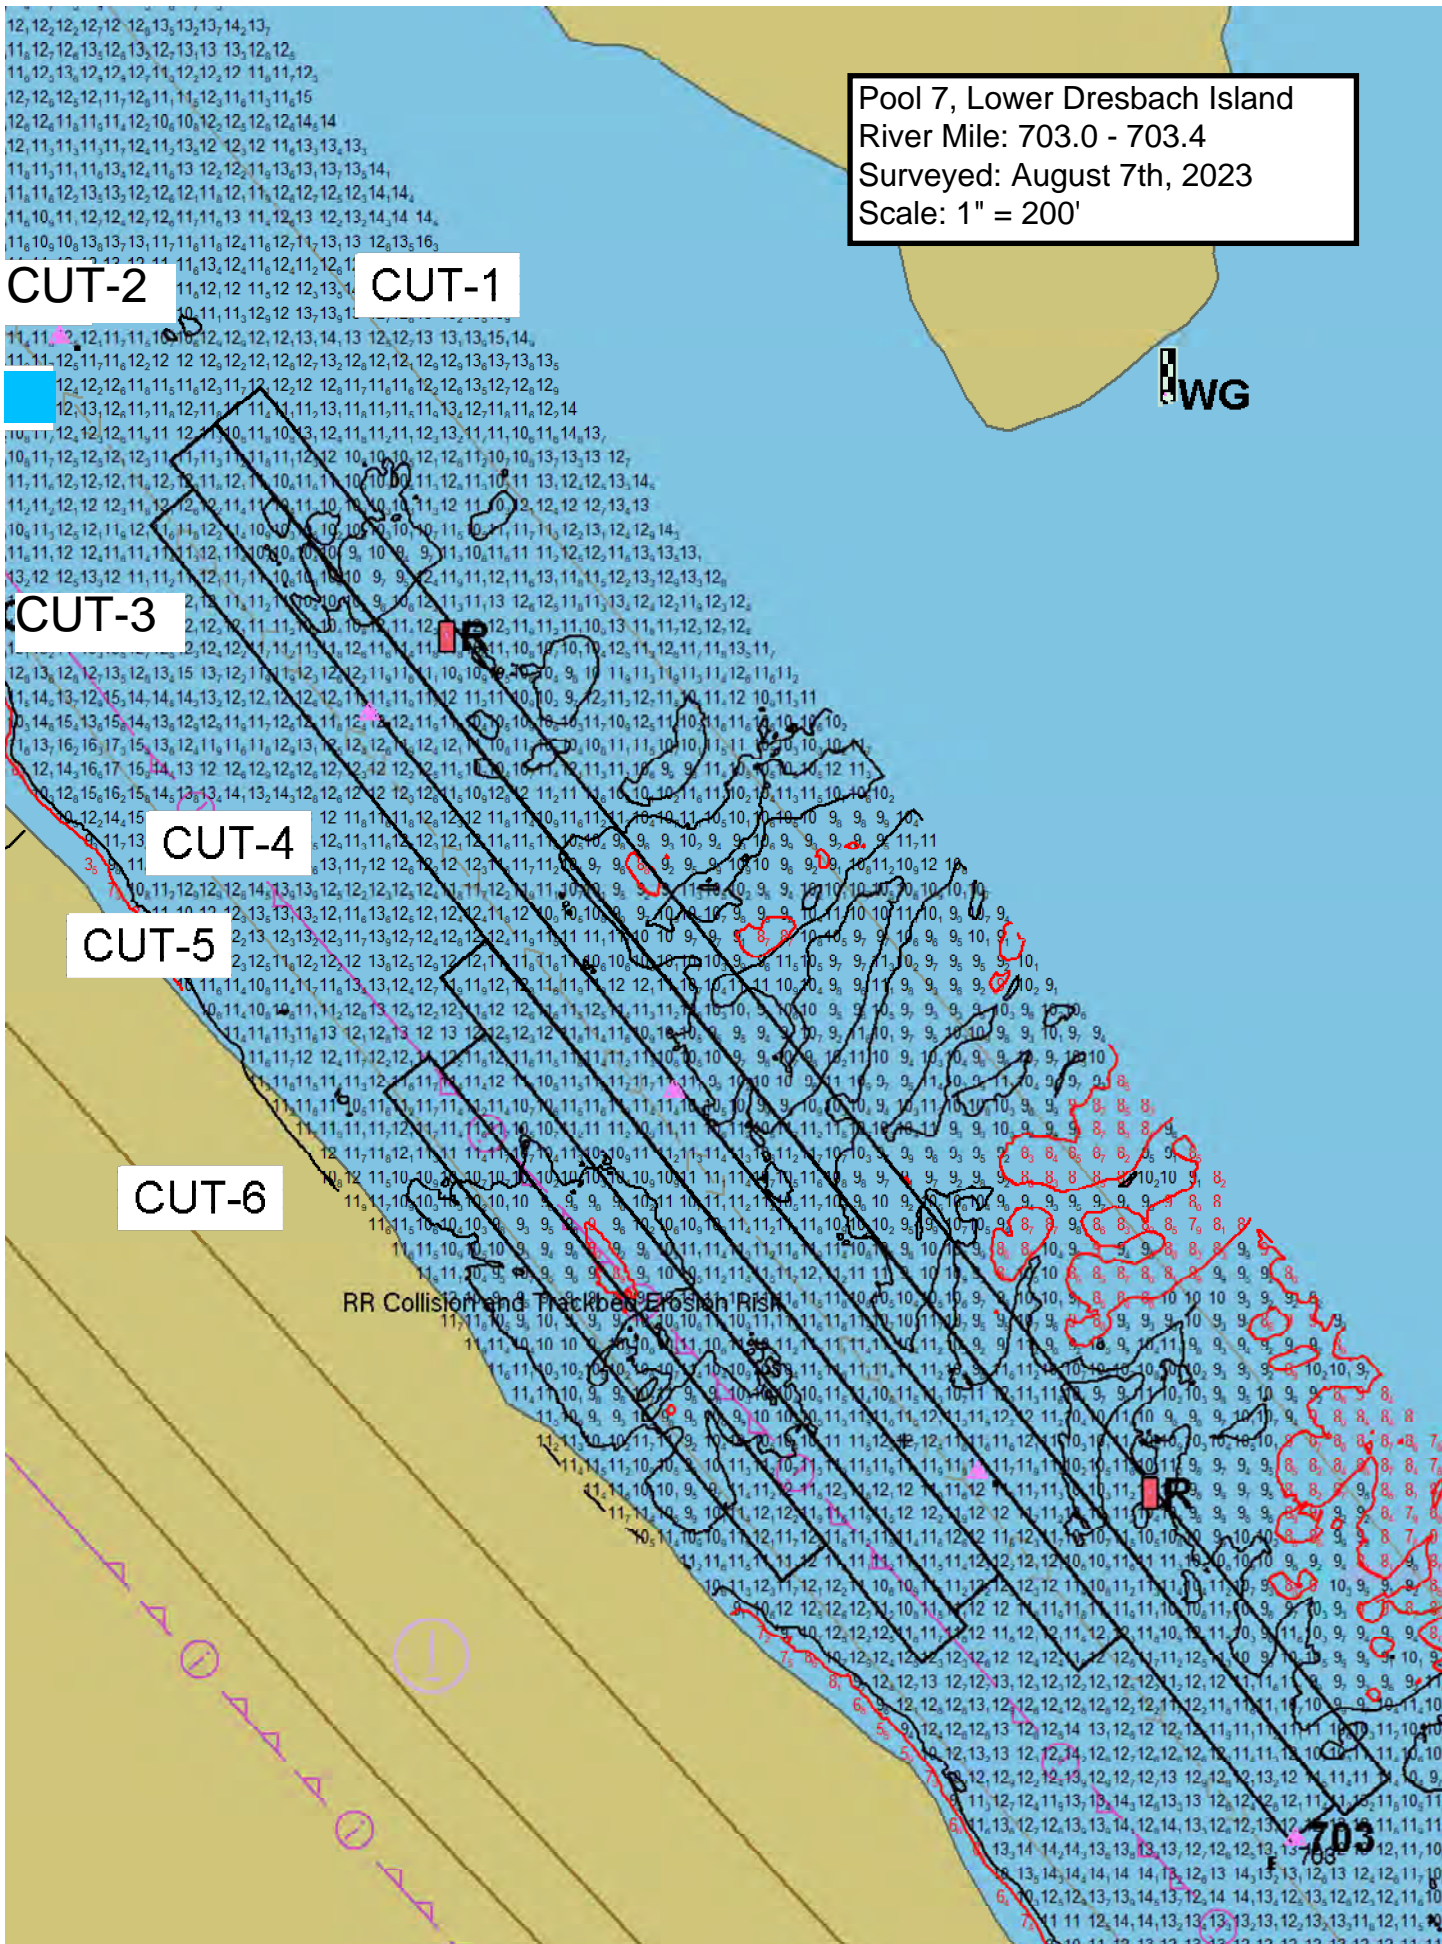

Pool 7, Lower Dresbach Island
River Mile: 703.0 - 703.4
Surveyed: August 7th, 2023
Scale: 1" = 200'

Pool 7, Dakota Island Plmt Access
River Mile: 706.5
Surveyed: August 7th, 2023
Scale: 1" = 100'

ACCESS CUT - 1

ACCESS CUT - 2

CENTER ACCESS
HWG

