

DN 23-43

DREDGING NOTICE
U.S. ARMY CORPS OF ENGINEERS
ST. PAUL DISTRICT

NOTICE DATE: September 29 th , 2023	DREDGING CATEGORY: Imminent
MEETING DATE: If requested	MEETING TIME:
BOAT REQUIREMENT:	MEETING LOCATION:
<hr/>	
DREDGE CUT NAME: Mouth of the MN River	RIVER MILE: MN River 0.6 – 1.0

HISTORIC DATA

Frequency: 4 %	Avg. Quantity/Job: 16,117 yd ³
Last Date Dredged: November 15 th , 1993	Avg. Quantity/Year: 608 yd ³

SURVEY DATA

Date Surveyed: September 21st, 2023
Water Surface Elevation: 686.8
Low Control Pool Elevation: 686.8
Net Difference: +0.0'
5 Day River Forecast: holding steady

DREDGING DATA

Recommended Channel Width: 100 feet
Recommended Dredging Depth: 12 feet
Estimated Quantity: 19,134 yd³ plus 46 yd³ for placement site access
Type of Dredge: Contract Mechanical Plant 2
Proposed Dredging Date: October 2nd, 2023
Estimated Duration: 10 dredging days
Justification for Dredging: The navigation channel is reduced to 155' between the 9.0' contours and closed between the 10.5' contours.


MATERIAL PLACEMENT DATA

Proposed Placement Site: Cargill East River
Location: MN-14.1-RMP
Site Characteristics: This is an upland beneficial use stockpile site provided to the Corps by the Lower MN River Watershed District.

If you have any questions concerning this project or want to request an on-site meeting please call me at (651) 290-5155.

Dan Cottrell
Dredging Manager

MN River, Mouth of the MN River
River Mile: 0.6 - 1.0
Surveyed: September 21st, 2023
Scale: 1" = 200'

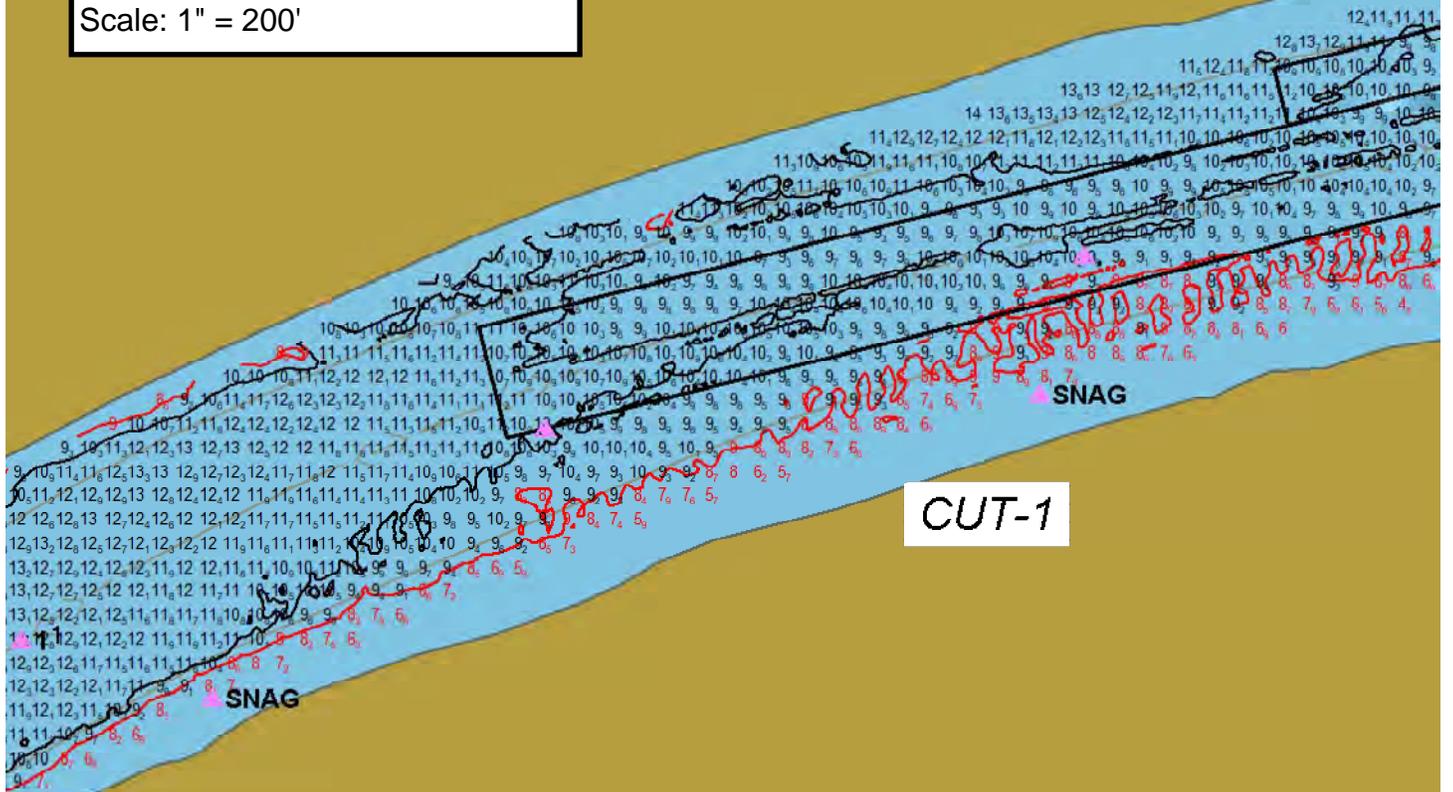

CUT-1

+

CUT-2

